
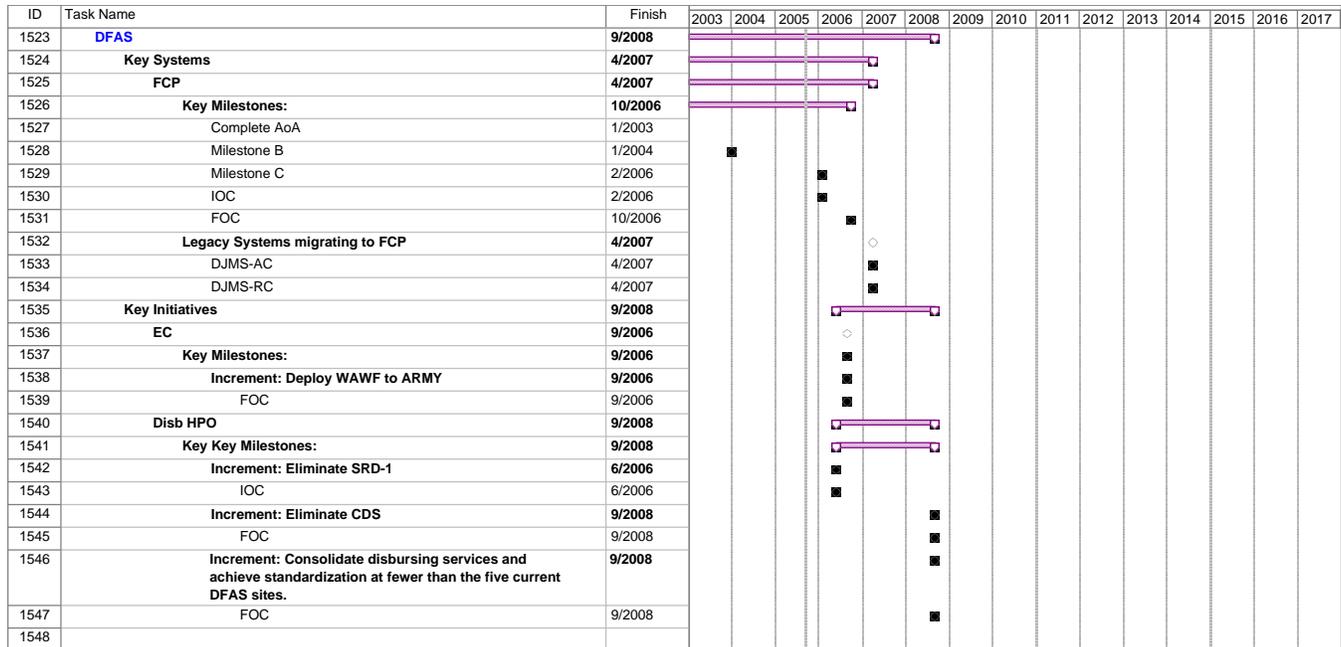


## Appendix J: System Transition Schedule

This appendix contains a Gantt Chart that shows system and initiative deployment milestones as well as system migration and retirement milestones. The chart groups systems and initiatives by Business Enterprise Priority (BEP) and by Component.

### EXAMPLE

The following is a roll-up of the BEP and Component schedules. One of the BEPs, Common Supplier Engagement and one of the Components, DFAS is expanded to show the degree of detail included within each of the BEP and Component activities.

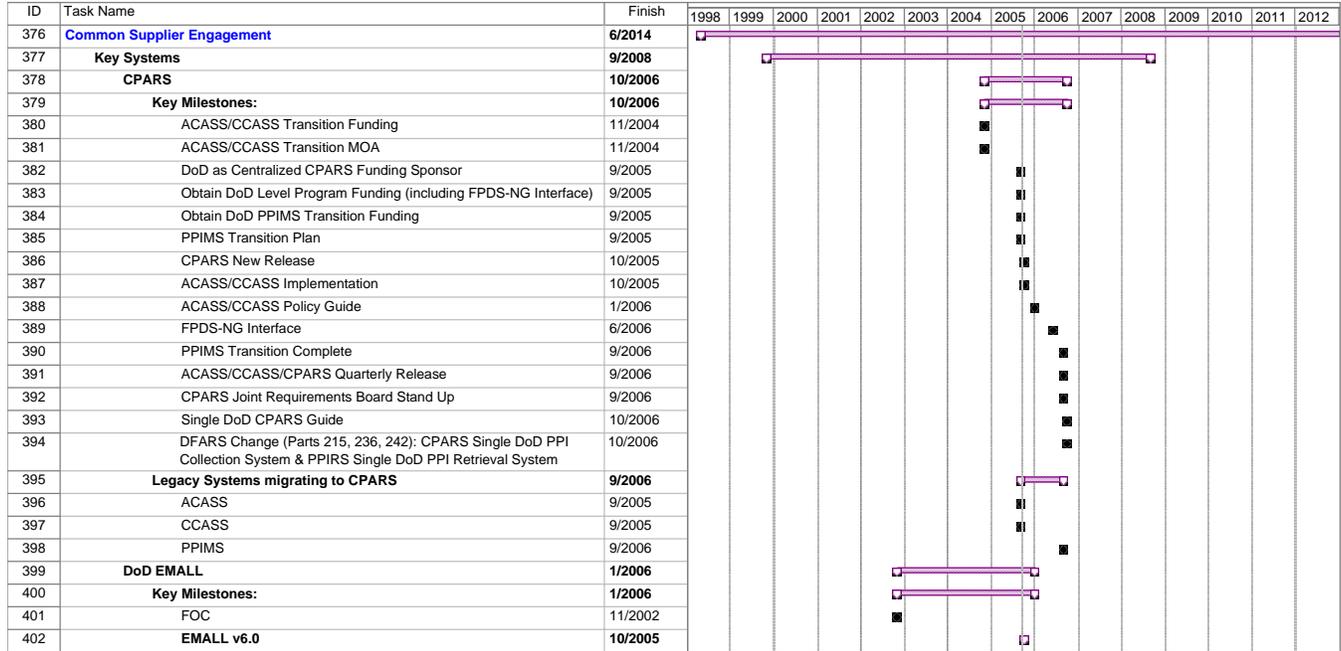

(This page is intentionally left blank)

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1	<b>BMMP</b>	<b>8/2008</b>												
2	<b>FM Support</b>	<b>9/2006</b>												
3	<b>Key Milestones:</b>	<b>9/2006</b>												
4	Begin deploying data standards (e.g., SFIS and unique identification (UID)) at the Department level that will enable data interoperability, traceability, visibility, and valuation of key assets as well as improve financial visibility and auditability	9/2006			◆									
5	Complete standard data element definitions to support managerial/cost	9/2006			◆									
6	Establish initial standards to integrate budgeting with execution financial	9/2006			◆									
7	Begin providing standards-based enterprise-level Program and Budget data definitions and business rules for Acquisition Category (ACAT) 1 Major Defense Acquisition Programs (MDAPs)	9/2006			◆									
8	Via Business Enterprise Information Services (BEIS) employ enterprise-level business intelligence, including management dashboards and drill down from summary to detail capability, for initial usage for select Components and the OSD.	9/2006			◆									
9	Implement DoD-level Financial Improvement and Audit Readiness (FIAR) Plan with Components to achieve clean audit opinions for balance sheet items that represent the largest asset and liability categories; integrate this plan with the BMMP systems TP.	9/2006			◆									
10	<b>P&amp;R Support</b>	<b>12/2006</b>												
11	<b>Key Milestones:</b>	<b>12/2006</b>												
12	Initial spiral release of integrated military personnel and pay management capability for Army	9/2006			◆									
13	Begin standardizing personnel information generated from a set of common personnel processes and business rules across the Components	9/2006			◆									
14	Initial deployment of Composite Health Care System (CHCS) II	12/2006				◆								
15	Release of fully operational Defense Travel System (DTS)	9/2006			◆									
16	<b>RP Support</b>	<b>9/2006</b>												
17	<b>Key Milestones:</b>	<b>9/2006</b>												
18	Complete Iteration 1 Initiatives - as described in other workbooks	TBD												
19	Standardize processes and data for management of real property inventories (Sept 06)	TBD												
20	Ongoing management efforts	TBD												
21	Complete linkage of environmental requirements with real property inventory (Sept 06)	TBD												
22	In accordance with Iteration 1 plans.	TBD												
23	Operate IRB, and continue to enhance portfolio (Ongoing)	TBD												
24	Complete Iteration 2 Plan	9/2006			◆									
25	DDESB BPR Complete	9/2006			◆									
26	<b>SC Support</b>	<b>9/2006</b>			◆									
27	<b>Key Milestones:</b>	<b>9/2006</b>			◆									
28	First spiral release of Defense Acquisition Management Information Retrieval (DAMIR), the initiative to provide enterprise-level visibility to acquisition program information, with Defense Acquisition Executive Summary (DAES)	9/2006			◆									

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
29	Release of Purview, an executive information system (part of DAMIR) that provides Selected Acquisition Reports (SAR) to include electronic SAR	9/2006			◆									
30	Final improvements to USXPORTS, a system that expedites the license application decision process while concurrently improving protection of national security interests and industry proprietary data.	9/2006			◆									
31	Complete valuations on 95 percent of military equipment programs	9/2006			◆									
32	Begin integrating standard Item Unique Identifier (IUID) data into target systems, ensure all new Government Furnishing Property (GFP) on solicitations meet IUID requirements	9/2006			◆									
33	Provide RFID tagging for Class I commodities and Classes IIIP, IV, V, VII, VIII, and IX shipments to distribution depots, aerial ports, and maintenance facilities	9/2006			◆									
34	Fully deploy the Electronic Subcontract Reporting System (eSRS) and the Federal Procurement Data System – Next Generation (FPDS-NG) as part of the Integrated Acquisition Environment	9/2006			◆									
35	Deploy Release 4.2.3 of the Standard Procurement System (SPS), which is the backbone of the DoD enterprise contracting and procurement activities. Release 4.2.3 is an enhanced, web-based version of SPS that will provide cross-Component support.	9/2006			◆									
36	Fully deploy Wide Area Workflow (WAWF). WAWF provides the ability to process invoices and receiving rpts electronically through the acceptance and payment process and serves as a collection point for the Unique Identification (IUID) information.	9/2006			◆									
37	<b>TSO</b>	<b>8/2008</b>												
38	<b>Key Milestones:</b>	<b>8/2008</b>												
39	(Communications) Congressional Committee Hearings	6/2005		◆										
40	Develop and implement pre 3.0 BEA IRB/DBSMC procedures	7/2005		◆										
41	Identify pre-certification authorities for IRB Process	7/2005		◆										
42	ETP	9/2005		◆										
43	DBSAE Selection	9/2005		◆										
44	Develop IRB Charters	9/2005		◆										
45	Implement initial capability to track certification to life-cycle	9/2005		◆										
46	Publish Business Transformation Planning Guidance	10/2005		◆										
47	Develop initial IRB/DBSMC Certification/portfolio management Metrics	10/2005		◆										
48	BEA Integration sessions	11/2005		◆										
49	Issue revised IRB policy documentation	11/2005		◆										
50	Develop and implement post 3.0 BEA IRB/DBSMC procedures	11/2005		◆										
51	Provide BMA requirements document to NII to establish long term capability to track systems budget, compliancy, certification, portfolio management, and information to meet various DoD reporting requirements	12/2005		◆										
52	Conduct progress review of BMMP systems/initiatives	12/2005		◆										
53	BEA Integration sessions	1/2006		◆										
54	Develop and Complete Architecture Assessment Guide	1/2006		◆										
55	Establish BMMP Test and Evaluation Artifact Repository	2/2006		◆										

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
56	(Communications) Annual Report to Congress	3/2006			◆									
57	Conduct progress review of BMMP systems/initiatives	3/2006			◆									
58	Publish Initial and Complete Integrated Enterprise Project Management (EPM) Schedules for the DoD BMMP Program	3/2006			◆									
59	ETP	3/2006			◆									
60	Publish Business Transformation Planning Guidance	3/2006			◆									
61	Establish capability to support DoD Business Transformation Collaborative Environment users. Initial capability:1000 users; Full capability: 2000 users.	3/2006			◆									
62	BEA Releases	3/2006			◆									
63	Complete Federated Plan and establish linkage for at least 1 component	3/2006			◆									
64	Publish and update Collaborative Architecture Development Tools/Guidance	3/2006			◆									
65	Gap analysis/resolution to identify future areas of focus for BEA development	3/2006			◆									
66	Automated Certification Pilot and Release in support of IRB Process	3/2006			◆									
67	BEA Integration sessions	5/2006			◆									
68	BEA Integration sessions	7/2006			◆									
69	ETP	9/2006			◆									
70	Conduct progress review of BMMP systems/initiatives	9/2006			◆									
71	Publish Initial and Complete Integrated Enterprise Project Management (EPM) Schedules for the DoD BMMP Program	9/2006			◆									
72	Establish capability to support DoD Business Transformation Collaborative Environment users. Initial capability:1000 users; Full capability: 2000 users.	9/2006			◆									
73	Complete annual review of Business System Investments	9/2006			◆									
74	Add Key Performance Indicator capability to BEA to align with OMB FEA (PRM)	9/2006			◆									
75	Publish Service Oriented Architecture Strategy	9/2006			◆									
76	Publish and update Collaborative Architecture Development Tools/Guidance	9/2006			◆									
77	Gap analysis/resolution to identify future areas of focus for BEA development	9/2006			◆									
78	BEA Releases	9/2006			◆									
79	Annual review of IRB/DBSMC Process and Procedures	10/2006			◆									
80	Issue revised IRB Policy documentation (if required)	11/2006			◆									
81	(Communications) Annual Report to Congress	3/2007				◆								
82	(Communications) Annual Report to Congress	3/2007				◆								
83	Update Architecture Assessment Guide	2/2007				◆								
84	Transition KPIs to MOEs	3/2007				◆								
85	Incorporate Service Oriented Architecture Principles into the BEA	3/2007				◆								
86	Incorporate Core Business Enterprise Services into the BEA	3/2007				◆								
87	Gap analysis/resolution to identify future areas of focus for BEA development	3/2007				◆								
88	Publish and update Collaborative Architecture Development Tools/Guidance	3/2007				◆								

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
89	BEA Releases	3/2007				◆								
90	BEA Releases	9/2007				◆								
91	Complete annual review of Business System Investments	9/2007				◆								
92	Annual review of IRB/DBSMC Process and Procedures	10/2007				◆								
93	Conduct progress review of BMMP systems/initiatives	12/2007				◆								
94	Update Architecture Assessment Guide	8/2008					◆							
95														
96	<b>Personnel Visibility</b>	<b>9/2011</b>												
97	<b>Key Systems</b>	<b>9/2011</b>												
98	<b>CHCS II</b>	<b>9/2011</b>												
99	<b>Key Milestones:</b>	<b>9/2011</b>												
100	<b>Increment: Block I</b>	<b>12/2006</b>												
101	Milestone C	1/2003												
102	IOC	9/2004	◆											
103	Initial Full Deployment Decision Review (FDDR)	11/2003												
104	FOC	12/2006				◆								
105	<b>Increment: Block II</b>	<b>3/2008</b>												
106	Milestone B	1/2003												
107	Initial Full Deployment Decision Review (FDDR)	5/2005		◆										
108	FOC	3/2008					◆							
109	<b>Increment: Block III</b>	<b>9/2011</b>												
110	Milestone A	1/2003												
111	Milestone B	3/2006			◆									
112	Milestone C	9/2007				◆								
113	Initial Full Deployment Decision Review (FDDR)	3/2008					◆							
114	FDDR, Release 2	3/2008					◆							
115	FDDR, Release 3	12/2008						◆						
116	FDDR, Release 4	9/2009							◆					
117	FOC	9/2011								◆				
118	<b>Legacy Systems migrating to CHCS II</b>	<b>9/2011</b>												
119	CHCS	9/2011												
120	CIS	9/2011												
121	CIW	5/2005		◆										
122	PHCA	3/2005		◆										
123	SRTS I	6/2007				◆								
124	<b>DCPDS</b>	<b>9/2004</b>												
125	<b>Key Milestones:</b>	<b>9/2004</b>												
126	Initial Policy	9/1993												
127	Milestone A	9/1997												
128	Plan Organizational & Role Change	9/1997												
129	Revise Policy	9/1998												

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
130	Detailed design of processes, testing and integrating those processes.	6/1999												
131	Milestone B	9/1999												
132	IOC (for Process)	10/1999												
133	IOC	10/1999												
134	Milestone C	3/2002												
135	FOC	9/2002												
136	Final Policy Implemented	9/2002												
137	Execute Organizational and Role Change	9/2002												
138	Train Personnel	9/2002												
139	FOC (for Process)	9/2002												
140	Certify Compliance to Policy	9/2004												
141	<b>DIMHRS</b> *Note: The DIMHRS program is being re-baselined and as a result the dates may change. Any changes will be incorporated in the next version	<b>7/2008</b>												
142	<b>Key Milestones:</b>	<b>7/2008</b>												
143	Initial Policy	1/1997												
144	Process Design Test & Integration	5/2002												
145	Certify Compliance to Policy	4/2003												
146	Milestone A	6/2004	◆											
147	Milestone B	3/2005		◆										
148	Milestone C	1/2006			◆									
149	IOC	3/2007				◆								
150	FOC	7/2008					◆							
151	Air Force Deployment	7/2007					◆							
152	Navy/Marine Corps Deployment	12/2007						◆						
153	<b>Legacy Systems migrating to DIMHRS</b>	<b>5/2007</b>												
154	AGRMIS	10/2006				◆								
155	AGRMIS-INFORMIX	10/2006				◆								
156	AMIS	1/2007				◆								
157	AMIS (J011)	1/2007				◆								
158	AORS	10/2006				◆								
159	APAS-E	10/2006				◆								
160	ARACMIS	10/2006				◆								
161	ASK	10/2006				◆								
162	CAR	10/2006				◆								
163	COMM-CD	10/2006				◆								
164	DAMIS-FS	10/2006				◆								
165	DAMIS-HQ	10/2006				◆								
166	DCIPS	5/2007					◆							
167	DJMS-AC	5/2007					◆							
168	DJMS-RC	5/2007					◆							
169	DMO	5/2007					◆							

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
170	EBM	10/2006			◆									
171	EDAS	10/2006			◆									
172	EDMIS	5/2007				◆								
173	EDTM	10/2006			◆									
174	eMILPO	10/2006			◆									
175	EPM	10/2006			◆									
176	ERS	10/2006			◆									
177	FCP	5/2007				◆								
178	ICDT	10/2006			◆									
179	IMAPMIS	5/2007				◆								
180	IMPS/IAOS/BWCO	1/2007				◆								
181	INPROC/OUTPROC/RUU	10/2006			◆									
182	ITAPDB	10/2006			◆									
183	IWS-2XC	10/2006			◆									
184	IWS-ACT	10/2006			◆									
185	IWS-AFS	10/2006			◆									
186	IWS-AGR/Calvin	10/2006			◆									
187	IWS-CEP	10/2006			◆									
188	IWS-CFP	10/2006			◆									
189	IWS-COM	10/2006			◆									
190	IWS-EBS	10/2006			◆									
191	IWS-INT	10/2006			◆									
192	IWS-PIC	10/2006			◆									
193	IWS-PNS	10/2006			◆									
194	IWS-RCCS	10/2006			◆									
195	IWS-SMS	10/2006			◆									
196	IWS-SMS-Cases	10/2006			◆									
197	IWS-SMSV-PERMS-I	10/2006			◆									
198	IWS-SMSV-ROTCAM	10/2006			◆									
199	IWS-SMSV-SGLI	10/2006			◆									
200	IWS-SMSV-SPA	10/2006			◆									
201	IWS-SMSV-STC	10/2006			◆									
202	IWS-SMSV-TTADS	10/2006			◆									
203	IWS-SOQ	10/2006			◆									
204	IWS-SPS	10/2006			◆									
205	IWS-TAM	10/2006			◆									
206	JUSTIS	10/2006			◆									
207	KEYSTONE-KEYVIEW-CS	10/2006			◆									
208	KEYSTONE-RETAIN-CS	10/2006			◆									
209	MBIS	10/2006			◆									
210	MCTFS-P	5/2007				◆								

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
211	MCTFS-P	5/2007				◆								
212	MGIB	10/2006												
213	MiLPDS	1/2007				◆								
214	MOBLAS	10/2006												
215	MOBPERS	10/2006				◆								
216	MYPAY	5/2007					◆							
217	NES	5/2007					◆							
218	NMPDS	5/2007					◆							
219	NMPDS-AMSAS	5/2007					◆							
220	NMPDS-DMRS	5/2007					◆							
221	NMPDS-EAIS	5/2007					◆							
222	NMPDS-EDPROJ II	5/2007					◆							
223	NMPDS-EDVR	5/2007					◆							
224	NMPDS-EPRES	5/2007					◆							
225	NMPDS-FSSS	5/2007					◆							
226	NMPDS-JASS	5/2007					◆							
227	NMPDS-LOOMIS	5/2007					◆							
228	NMPDS-NAVACTSTAT	5/2007					◆							
229	NMPDS-NMPE	5/2007					◆							
230	NMPDS-OAIS II	5/2007					◆							
231	NMPDS-ODIS	5/2007					◆							
232	NMPDS-ODMS	5/2007					◆							
233	NMPDS-OISS	5/2007					◆							
234	NMPDS-ORGSUPP	5/2007					◆							
235	NMPDS-TADTRACK	5/2007					◆							
236	NMPDS-TASM	5/2007					◆							
237	NOWS	5/2007					◆							
238	NSIPS	5/2007					◆							
239	ODS	10/2006				◆								
240	OLDS	5/2007					◆							
241	OOR	10/2006				◆								
242	OPINS	5/2007					◆							
243	PC-III	1/2007					◆							
244	PDCAPS	10/2006				◆								
245	PEPDUS	10/2006				◆								
246	PERSLOC	10/2006				◆								
247	PERSTEMPO	10/2006				◆								
248	PIM	10/2006				◆								
249	PRMS	10/2006				◆								
250	QMP-CS	10/2006				◆								
251	RDMS	10/2006				◆								

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
252	RDMS- Suite	10/2006			◆									
253	RECBASS-R	10/2006			◆									
254	RHS	5/2007				◆								
255	RIS	10/2006			◆									
256	RLAS	10/2006			◆									
257	ROAMS	10/2006			◆									
258	RPAM	10/2006			◆									
259	RPAS	10/2006			◆									
260	RRS	10/2006			◆									
261	RSAS/RCCPDS	10/2006			◆									
262	RSDQ	10/2006			◆									
263	RVPS	10/2006			◆									
264	SAM	5/2007				◆								
265	SEPM	10/2006			◆									
266	SIDPERS-ARNG	10/2006			◆									
267	SLO	10/2006			◆									
268	SMS	10/2006			◆									
269	SRB	10/2006			◆									
270	SRT	10/2006			◆									
271	TAPDB-AE	10/2006			◆									
272	TAPDB-AO	10/2006			◆									
273	TAPDB-ARNG	10/2006			◆									
274	TAPDB-R	10/2006			◆									
275	TDRL (AR)	10/2006			◆									
276	TMTS	1/2007				◆								
277	TOPMIS	10/2006			◆									
278	TOPMIS II	10/2006			◆									
279	TOPTUS	10/2006			◆									
280	TPS	10/2006			◆									
281	TRANSPROC	10/2006			◆									
282	UD/MIPS	5/2007				◆								
283	UIC	5/2007				◆								
284	UMIDS	5/2007				◆								
285	UPDB (USAREUR)	10/2006			◆									
286	UPDB-Assignments	10/2006			◆									
287	UPDB-CPAS	10/2006			◆									
288	UPDB-CPF	10/2006			◆									
289	UPDB-FSTE-2	10/2006			◆									
290	UPDB-Locator	10/2006			◆									
291	UPDB-Personnel Detachment	10/2006			◆									
292	UPDB-Retention	10/2006			◆									

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
293	UPDB-S-Gate	10/2006			◆									
294	UPDB-Soldiers' Page	10/2006			◆									
295	UPDB-Sponsorship	10/2006			◆									
296	UPDB-Sponsorship Training	10/2006			◆									
297	UPDB-Strength Management	10/2006			◆									
298	UPDB-TCS	10/2006			◆									
299	UPDB-TRACS	10/2006			◆									
300	vMPF	1/2007				◆								
301	WWL	10/2006			◆									
302	ZIP-GLC	10/2006			◆									
303	<b>DTS</b>	<b>9/2007</b>	▨											
304	<b>Key Milestones:</b>	<b>9/2006</b>	▨											
305	Initial policy	12/1995												
306	Complete AoA	6/1997												
307	Final Policy Implemented	5/2002												
308	Milestone C	10/2003												
309	IOC	12/2003												
310	IOC (for Process)	12/2003												
311	FOC	9/2006			◆									
312	Execute Organizational and Role Change	9/2006			◆									
313	Train Personnel	9/2006			◆									
314	Process Design Test & Integration	9/2006			◆									
315	FOC (for Process)	9/2006			◆									
316	Plan Organizational & Role Change	9/2006			◆									
317	<b>Legacy Systems migrating to DTS</b>	<b>9/2007</b>	▨											
318	AGTR 2002	10/2005		◆										
319	ATOS	9/2006			◆									
320	CTS	9/2006			◆									
321	DFAS-OW	9/2007				◆								
322	DTOS	9/2006			◆									
323	ETS	9/2006			◆									
324	FAST	9/2006			◆									
325	GAFS-DTS	9/2006			◆									
326	GENUS	TBD		◆										
327	IATS	9/2005		◆										
328	MSC-T&T	9/2006			◆									
329	MTS	9/2006			◆									
330	NEAMIS	TBD		◆										
331	Order Writer	TBD		◆										
332	PDA	9/2006			◆									
333	PRODS	9/2006			◆									

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	
334	RATS	9/2006			◆										
335	ROWS	9/2006			◆										
336	RTS	9/2006			◆										
337	TMP	9/2006			◆										
338	TOPS	5/2005		◆											
339	TR	9/2006			◆										
340	TRAVEL	3/2005		◆											
341	UFTS/4001	9/2006			◆										
342	ULNATIS	9/2006			◆										
343	WinATOS	9/2006			◆										
344															
345	<b>Acquisition Visibility</b>	<b>6/2007</b>													
346	<b>Key Systems</b>	<b>2/2006</b>													
347	<b>USXPORTS</b>	<b>2/2006</b>													
348	<b>Key Milestones:</b>	<b>1/2006</b>													
349	Milestone A	8/2001													
350	Complete AoA	4/2002													
351	USXPORTS Sys Architecture Doc	3/2003													
352	Test and Evaluation Master Plan	8/2003													
353	Interoperability Certification of ORD	9/2003													
354	Testable Enterprise System	10/2003													
355	Deployable Enterprise System	5/2004	◆												
356	IOC	6/2004	◆												
357	USXPORTS V1.0	6/2004	◆												
358	USXPORTS V2.0	12/2004		◆											
359	USXPORTS V2.1	1/2005		◆											
360	USXPORTS V3.0	5/2005		◆											
361	USXPORTS V3.1	9/2005		◆											
362	USXPORTS V4.0	1/2006			◆										
363	FOC	1/2006			◆										
364	<b>Legacy systems migrating to USXPORTS</b>	<b>2/2006</b>			◆										
365	TPS	2/2006			◆										
366	<b>Key Initiatives</b>	<b>6/2007</b>													
367	<b>DAMIR</b>	<b>6/2007</b>													
368	<b>Key Milestones:</b>	<b>6/2007</b>													
369	Unclassified SAR data to be provided to Congress electronically via DAMIR Purview. Classified SAR data to be provided to Congress via a classified annex. Elimination of the paper SAR submission.	12/2005			◆										
370	Service components allow OSD to pull SAR, DAES and APB information directly from their Service Acquisition Information Systems via DAMIR web services rather than entering data into CARS	9/2005		◆											

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
371	Update DAES Policy based on IPT Recommendations	12/2005			◆									
372	Determine and Implement New Business Rules	TBD												
373	Electronic SARs to Congress (retire paper SAR submission process)	4/2006			◆									
374	Incorporate DAES IPT Recommendations	6/2007				◆								
375														
376	<b>Common Supplier Engagement</b>	<b>6/2014</b>												
377	<b>Key Systems</b>	<b>9/2008</b>												
378	<b>CPARS</b>	<b>10/2006</b>												
379	<b>Key Milestones:</b>	<b>10/2006</b>												
380	ACASS/CCASS Transition Funding	11/2004	◆											
381	ACASS/CCASS Transition MOA	11/2004	◆											
382	DoD as Centralized CPARS Funding Sponsor	9/2005		◆										
383	Obtain DoD Level Program Funding (including FPDS-NG Interface)	9/2005		◆										
384	Obtain DoD PPIMS Transition Funding	9/2005		◆										
385	PPIMS Transition Plan	9/2005		◆										
386	CPARS New Release	10/2005		◆										
387	ACASS/CCASS Implementation	10/2005		◆										
388	ACASS/CCASS Policy Guide	1/2006			◆									
389	FPDS-NG Interface	6/2006			◆									
390	PPIMS Transition Complete	9/2006			◆									
391	ACASS/CCASS/CPARS Quarterly Release	9/2006			◆									
392	CPARS Joint Requirements Board Stand Up	9/2006			◆									
393	Single DoD CPARS Guide	10/2006			◆									
394	DFARS Change (Parts 215, 236, 242): CPARS Single DoD PPI Collection System & PPIRS Single DoD PPI Retrieval System	10/2006			◆									
395	<b>Legacy Systems migrating to CPARS</b>	<b>9/2006</b>												
396	ACASS	9/2005		◆										
397	CCASS	9/2005		◆										
398	PPIMS	9/2006			◆									
399	<b>DoD EMALL</b>	<b>1/2006</b>												
400	<b>Key Milestones:</b>	<b>1/2006</b>												
401	FOC	11/2002												
402	<b>EMALL v6.0</b>	<b>10/2005</b>												
403	Website Overhaul	10/2005		◆										
404	Consolidation into one physical location	10/2005		◆										
405	User Interface Enhancements	10/2005		◆										
406	<b>EMALL v6.1</b>	<b>1/2006</b>												
407	Improvements to DLA orders	1/2006			◆									
408	<b>EDA</b>	<b>4/2006</b>												
409	<b>Key Milestones:</b>	<b>4/2006</b>												

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
410	Release 6.2: Ability to receive contracts data from SPS for prepopulation of Wide Area Workflow	5/2005		◆										
411	EDA upgrade to Oracle 10g database and application server (AIS)	12/2005		◆										
412	Release of EDA, merging capabilities and users from EDA and NAFI	4/2006			◆									
413	<b>Legacy Systems migrating to EDA</b>	<b>4/2006</b>			◆									
414	NAFI	4/2006			◆									
415	<b>SPS</b>	<b>9/2008</b>												
416	<b>Key Milestones:</b>	<b>9/2008</b>												
417	<b>Increment 2 (v4.2.2)</b>	<b>2/2006</b>												
418	IOC	5/2003												
419	SRO6 Release - Incorporation of Major Weapons Systems Requirements	8/2005		◆										
420	Final Policy Implemented	4/2005		◆										
421	FOC	2/2006			◆									
422	<b>Increment 3 (v4.2.3)</b>	<b>9/2008</b>												
423	IOC	6/2006			◆									
424	Milestone C	2/2006			◆									
425	Web Based Technology	6/2006			◆									
426	Improved functionality for Major Weapon Systems	6/2006			◆									
427	Improved Adapter Technology	6/2006			◆									
428	Improved functionality for Inventory Control Point	6/2006			◆									
429	Full deployment across DoD	6/2006			◆									
430	FOC	9/2008					◆							
431	<b>Legacy Systems migrating to SPS</b>	<b>TBD</b>												
432	ACPS	TBD												
433	AMAS	TBD												
434	AMIS	9/2004	◆											
435	CONWRITE (CWS)(J104)	TBD												
436	ITIMP	TBD												
437	PADDS	TBD												
438	<b>WAWF</b>	<b>9/2006</b>												
439	<b>Key Milestones:</b>	<b>9/2006</b>												
440	<b>Increment: v3.0.7 Release</b>	<b>9/2006</b>												
441	IOC (for Process)	11/1999												
442	Achievement of Initial Policy implementation.	7/2003												
443	Final Policy Implemented	1/2005		◆										
444	Enhanced DCAA Audit Features	6/2005		◆										
445	Enhanced Document rejection capabilities	6/2005		◆										
446	Integration with DLA DSS logistics system	6/2005		◆										
447	IOC	9/2005		◆										
448	FOC	9/2006			◆									
449	<b>Increment: v3.0.8 Release</b>	<b>7/2005</b>		◆										

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
450	Miscellaneous Payment functionality	7/2005		◆										
451	Contract Pre-population from SPS via EDA	7/2005		◆										
452	Enhanced Document rejection capabilities	7/2005		◆										
453	<b>Increment: v.3.0.9 Release</b>	<b>12/2005</b>		▽										
454	Capability to track Government Furnished Property	12/2005		◆										
455	Enhanced UID processing capability	12/2005		◆										
456	Ability to view Financial payment status ("My Invoice" Link)	12/2005		◆										
457	DSS Phase II (partial) and 861 to BSM	12/2005		◆										
458	<b>Key Initiatives</b>	<b>6/2014</b>		▨										
459	<b>CC-SF44</b>	<b>11/2006</b>		▽	▨	▽								
460	<b>Key Milestones:</b>	<b>11/2006</b>		▽	▨	▽								
461	<b>Increment: Phase 1</b>	<b>2/2006</b>		▽	▨	▽								
462	Integration award	6/2005		◆										
463	Demonstrate capability (Phase 1)	10/2005		◆										
464	First test unit equipped with functionality (Phase 1)	12/2005		◆										
465	IOC (Phase 1)	2/2006		◆										
466	<b>Increment: Phase 2</b>	<b>11/2006</b>			▽	▨	▽							
467	System Demonstration (Phase 2)	6/2006			◆									
468	1st unit equipped (Phase 2)	8/2006			◆									
469	IOC (Phase 2)	11/2006			◆									
470	<b>DBSE</b>	<b>6/2014</b>		▨										
471	<b>Key Milestones:</b>	<b>6/2014</b>		▨										
472	<b>Increment: Increment 1</b>	<b>9/2011</b>		▨										
473	Milestone A	1/2006		◆										
474	Milestone B	6/2008					◆							
475	Milestone C	9/2010								◆				
476	IOC	9/2010								◆				
477	FOC	9/2011									◆			
478	<b>Increment: Increment 2</b>	<b>3/2013</b>		▨										
479	Milestone A	1/2006		◆										
480	Milestone B	6/2010								◆				
481	Milestone C	3/2012										◆		
482	IOC	3/2012										◆		
483	FOC	3/2013											◆	
484	<b>Increment: Increment 3</b>	<b>6/2014</b>		▨										
485	Milestone A	1/2006		◆										
486	Milestone B	12/2011										◆		
487	Milestone C	6/2013											◆	
488	IOC	6/2013											◆	
489	FOC	6/2014												◆
490	<b>Federal IAE</b>	<b>12/2006</b>		▨										

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	
491	<b>CCR</b>	<b>10/2006</b>													
492	<b>Key Milestones:</b>	<b>10/2006</b>													
493	Initial Policy	5/1998													
494	Final Policy Implemented	10/2003													
495	Deploy web-enabled socio-economic validations with SBA	5/2005													
496	Deploy web-enabled taxpayer identification number validations with IRS	10/2005													
497	All component systems interface to deploy CCR as true authoritative source	10/2006													
498	<b>EPLS</b>	<b>6/2005</b>													
499	<b>Key Milestones:</b>	<b>6/2005</b>													
500	Initiate Redesign efforts	6/2005													
501	Initial Policy	1/2005													
502	Final Policy Implemented	1/2005													
503	<b>eSRS</b>	<b>4/2006</b>													
504	<b>Key Milestones:</b>	<b>4/2006</b>													
505	OMB Guidance Published	3/2005													
506	IOC	5/2005													
507	Development IOC	8/2005													
508	Pilot Development	9/2005													
509	Development FOC	10/2005													
510	FAR Changes Finalized	10/2005													
511	DoD Deployment	4/2006													
512	<b>FBO</b>	<b>6/2005</b>													
513	<b>Key Milestones:</b>	<b>6/2005</b>													
514	Final Policy Implemented	1/2002													
515	Award of FBO Recompete	6/2005													
516	<b>Legacy Systems migrating to FBO</b>	<b>1/2003</b>													
517	Commerce Business Daily Online	1/2003													
518	<b>FedReg</b>	<b>9/2006</b>													
519	<b>Key Milestones:</b>	<b>9/2006</b>													
520	Initial policy	10/2003													
521	IOC	1/2003													
522	Inclusion of Fiscal Station Number (FSN)	8/2005													
523	DoD begins transition to using FedReg online	9/2005													
524	DoD uses FedReg as authoritative source of intra-governmental buyer/seller info	9/2006													
525	<b>FedTeDS</b>	<b>12/2005</b>													
526	<b>Key Milestones:</b>	<b>12/2005</b>													
527	FOC	3/2003													
528	FedTeDS Coop Site	12/2005													
529	Expected Approval of FAR Case	10/2005													

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
530	<b>FPDS-NG</b>	<b>10/2006</b>												
531	<b>Key Milestones:</b>	<b>10/2006</b>												
532	Finalize FAR changes	9/2005												
533	Achieve the full operating capability (for process)	10/2005												
534	DFARS/PGI changes finalized for new NG capabilities	10/2005												
535	Full deployment of machine to machine capability within DoD	10/2006												
536	<b>Legacy Systems migrating to FPDS-NG</b>	<b>TBD</b>												
537	FPDS	TBD												
538	<b>ORCA</b>	<b>12/2006</b>												
539	<b>Key Milestones:</b>	<b>12/2006</b>												
540	FAR Changes finalized instructing use	1/2005												
541	Include DFARS (DoD-level) data elements	9/2006												
542	Provide XML interface to perform data search and extracts	9/2006												
543	DLA complete deployment of ORCA	12/2006												
544	<b>PPIRS</b>	<b>9/2006</b>												
545	<b>Key Milestones:</b>	<b>9/2006</b>												
546	PPIRS-SR Pilot Completion	9/2005												
547	PPIRS-SR DoD Directive	10/2005												
548	DoD as Centralized Funding Sponsor	10/2005												
549	PPIRS-SR Joint Requirements Board Stand Up	10/2005												
550	Develop DoD PPIRS-SR Pilot	3/2006												
551	Deploy DoD PPIRS-SR Capability	9/2006												
552	<b>Legacy systems migrating to PPIRS</b>	<b>TBD</b>												
553	ABVS	TBD												
554	RYG	TBD												
555	<b>WDOL</b>	<b>6/2005</b>												
556	<b>Key Milestones:</b>	<b>6/2005</b>												
557	Dept. of Labor Finalize regulation changes	6/2005												
558	FOC	6/2005												
559	<b>Strategic Sourcing</b>	<b>11/2006</b>												
560	<b>ARM Pilot</b>	<b>4/2006</b>												
561	<b>Key Milestones:</b>	<b>4/2006</b>												
562	Proof of Concept	10/2005												
563	Advanced Requirements Management (ARM) Pilot: Design	11/2005												
564	Advanced Requirements Management (ARM) Pilot: Develop ARM Solution	3/2006												
565	Advanced Requirements Management (ARM) Pilot: Training	3/2006												
566	Conduct opportunity analysis	4/2006												
567	<b>ASAS</b>	<b>11/2006</b>												
568	<b>Key Milestones:</b>	<b>11/2006</b>												

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
569	Acquisition Spend Analysis Pilot (ASAP)/Service: - Migrate ASAP functionality to ETL/data mart solution; - Fix scalability and performance problems; - Add support concurrent users; - Add additional contract writing system data available in ACBIS and CBIS	5/2006			◆									
570	Acquisition Spend Analysis Pilot (ASAP)/Service: - Initial Production Deployment; - Implement data cleansing; - Enhance front-end analytics; - Expose additional data from all contract writing systems across AT&L (e.g., Army, Navy, AF, ODAs, etc)	11/2005		◆										
571	Second Production Deployment with Expanded capabilities	11/2006			◆									
572	<b>e-STRATS</b>	<b>9/2006</b>			▬									
573	<b>Key Milestones:</b>	<b>9/2006</b>			▬									
574	- Long Term: Planning and requirements development. Establishment of Joint Tiger Team to collaborate on DoD-wide capability/functionality; - Short Term: Approval, configuration, and use of SEAPORT-e as Interim Enterprise solution.	9/2005		◆										
575	- Long Term: Requirements evaluation for consideration under DBSE; - Short Term: On-going use of the SEAPORT-e interim solution.	3/2006			◆									
576	- Long Term: Requirements evaluation for consideration under DBSE; - Short Term: Continue use of SEAPORT-e until transition to a long term COTS system. Evaluate results.	9/2006			◆									
577														
578	<b>Matériel Visibility</b>	<b>12/2010</b>												
579	<b>Key Initiatives</b>	<b>12/2010</b>												
580	<b>MEV</b>	<b>12/2008</b>												
581	<b>Key Milestones:</b>	<b>12/2008</b>												
582	<b>Increment: Increment 1</b>	<b>12/2006</b>												
583	Complete AoA	5/2004	◆											
584	Milestone B	5/2005		◆										
585	Complete Principle-based Business Rules	9/2005		◆										
586	Incorporate in FMR MEV Business Rules	9/2005		◆										
587	Initial Program Valuations Completed (100% of total universe)	12/2005		◆										
588	IOC	6/2006			◆									
589	FY06 year end close using baseline valuation methodologies	9/2006			◆									
590	FOC	9/2006			◆									
591	Quarterly reporting of baseline valuation using baseline methodology. Newly acquired programs will be valued using a baseline methodology approach. This is a Quarterly recurring process.	12/2006			◆									
592	<b>Increment: Increment 2</b>	<b>12/2008</b>												
593	Milestone B	8/2006			◆									
594	IOC	9/2007				◆								
595	Milestone C	9/2007				◆								

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
596	Quarterly newly acquired programs will be valued using Increment 2 methodology. Total responsibility shifts to each Service & Other Defense Agencies	12/2008					◆							
597	<b>IUID</b>	<b>12/2010</b>	◆											
598	<b>Key Milestones:</b>	<b>12/2010</b>	◆											
599	Final Policy Implemented	12/2010							◆					
600	Initial policy	7/2003	◆											
601	IUID of New Items	1/2004	◆											
602	IUID of Legacy Items in Inventory and Operational Use	12/2004	◆											
603	IUID of DoD Property in the Possession of Contractors	5/2005		◆										
604	All new Government Furnished Property (GFP) on solicitations and contracts meet the IUID requirements (requires DFARS change).	1/2006			◆									
605	All Program Item Unique Identification (IUID) Implementation Plans and Automated Information System (AIS) plans to be completed and submitted to their respective Milestone Decision Authority.	1/2006			◆									
606	IUID STANAG ratification by NATO Asset Tracking Working Group.	3/2006			◆									
607	Full capability for electronic management of DoD property in the possession of contractors	10/2006				◆								
608	All serially managed assets registered in the IUID Registry, and fully integrated capability for uniquely identifying and marking of personal property items in all organic depots.	7/2007				◆								
609	Demonstrate an integrated data environment.	7/2007				◆								
610	Complete IUID marking of all items and embedded items.	12/2010							◆					
611	<b>MILS to EDI or XML</b>	<b>6/2007</b>	◆											
612	<b>Key Milestones:</b>	<b>6/2007</b>	◆											
613	Final policy Implemented	12/2003	◆											
614	Initial Policy	12/2003	◆											
615	DUSD(AT&L) 22 Dec 03 memorandum 'Migration to the Defense Logistics Management Standards (DLMS) and Elimination of the Military Standard Systems (MILS) provides appropriate policy support for this	12/2003	◆											
616	Allocate 1/2 funds to the highest priority interfaces	3/2006			◆									
617	Determine all DTS potential trading partner interfaces	3/2006			◆									
618	Monitor trading partner migration performance and provide assistance as appropriate	3/2006			◆									
619	Prioritize all potential interfaces	3/2006			◆									
620	Monitor trading partner migration performance and provide assistance as appropriate	9/2006				◆								
621	Allocate 2nd 1/2 of funds to next highest priority interfaces	9/2006				◆								
622	Assure successful implementation of migrated interfaces	9/2006				◆								
623	Monitor trading partner migration performance and provide assistance as appropriate	6/2007					◆							
624	Assure successful implementation of migrated interfaces	6/2007					◆							
625	<b>RFID</b>	<b>1/2007</b>	◆											
626	<b>Key Milestones:</b>	<b>1/2007</b>	◆											

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
627	Implement ability to read/write passive RFID at 1/4 of CONUS depots.	12/2005		◆										
628	Implement RFID at 3 aerial ports.	12/2005		◆										
629	Publish DFAR clause governing application of tags to Class I (some), II, VI, IX shipments to distribution depots, aerial ports, and maintenance facilities.	12/2005		◆										
630	Suppliers apply passive RFID tagging to items as listed above.	1/2006		◆										
631	Implement ability to read/write passive RFID at 1/4 of CONUS depots.	4/2006			◆									
632	Implement ability to read/write passive RFID at 1/4 of CONUS depots.	7/2006			◆									
633	Publish DFAR clause governing application of tags to remaining commodities and remaining locations.	12/2006				◆								
634	Suppliers apply passive RFID tags to all shipments for all commodities.	1/2007				◆								
635														
636	<b>Real Property Accountability</b>	<b>12/2010</b>		▨										
637	<b>Key Initiatives</b>	<b>12/2010</b>		▨										
638	<b>ELRV&amp;RR</b>	<b>10/2006</b>			▨									
639	<b>Key Milestones:</b>	<b>10/2006</b>			▨									
640	Complete Data Model	9/2006			◆									
641	Services begin implementation	10/2006			◆									
642	<b>HMPC&amp;IMR</b>	<b>12/2009</b>			▨									
643	<b>Key Milestones:</b>	<b>12/2009</b>			▨									
644	Requirements Document Phase I Released	3/2006			◆									
645	IOC of Product Hazard Data Master	3/2007				◆								
646	Initial Component Implementation	12/2009						◆						
647	<b>RPAR</b>	<b>3/2006</b>		▨										
648	<b>Key Milestones:</b>	<b>3/2006</b>		▨										
649	<b>Increment: Custody of Assest and Associated Data</b>	<b>3/2006</b>		▨										
650	Complete real property acceptance requirements	9/2005		◆										
651	Revised unified facilities criteria	3/2006			◆									
652	<b>RPIR</b>	<b>12/2007</b>		▨										
653	<b>Key Milestones:</b>	<b>12/2007</b>		▨										
654	<b>Increment: RPIR Implementation</b>	<b>12/2007</b>		▨										
655	Revised DFAR	9/2005		◆										
656	Revised 4165.14	9/2005		◆										
657	Revised FMR	9/2005		◆										
658	Scope the Increment 2 & 3 Milestones	3/2006			◆									
659	Outreach and training of modernized real property management practices	12/2007					◆							
660	Integration with component systems	12/2007					◆							
661	Incorporation of Standardized Data Elements in Authoritative Systems	TBD												

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
662	Incorporation of Standardized Data Elements in Authoritative Systems - 87 Data Elements	TBD												
663	Incorporation of Standardized Data Elements in Authoritative Systems (spiral 1)	TBD												
664	Incorporation of Standardized Data Elements in Authoritative Systems - Spiral 2	TBD												
665	Incorporation of Standardized Data Elements in Authoritative Systems - Spiral 3	TBD												
666	Complete analysis of Material Systems Alternatives	TBD												
667	Selection and implementation of a federated or centralized system solution	TBD												
668	<b>RPUID</b>	<b>12/2010</b>												
669	<b>Key Milestones:</b>	<b>12/2010</b>												
670	<b>Increment: Real Property Unique Identifier Registry Development, Maintenance and Integration with Other DoD Systems</b>	<b>12/2007</b>												
671	Policy for UIDs within DoD referencing the use of identifiers for real property	6/2005		◆										
672	Policies for the appropriate uses of Real Property Site and Asset Unique Identifiers	6/2005		◆										
673	IOC for Site Registry (not subject to formal milestone reviews)	12/2005			◆									
674	Outreach and training of modernized real property management practices	5/2006				◆								
675	IOC for Asset Registry (not subject to formal milestone reviews)	12/2006					◆							
676	Integration with Real Property financial systems	12/2007						◆						
677	FOC for Asset Registry (not subject to formal milestone reviews)	TBD												
678	Subsequent real property system spirals, in accordance with re-engineered processes	TBD												
679	Incorporation of Standardized Data Elements in Authoritative Systems	TBD												
680	Implementation of Analysis of Material Alternatives	TBD												
681	<b>Increment: Management of Geospatial Information</b>	<b>12/2010</b>												
682	Visualizer	12/2005		◆										
683	Data	12/2008						◆						
684	Geospatial depiction of All Land Parcels and Sites	12/2010								◆				
685														
686	<b>Financial Visibility</b>	<b>9/2009</b>												
687	<b>Key Systems</b>	<b>9/2009</b>												
688	<b>BEIS</b>	<b>9/2009</b>												
689	<b>Key Milestones:</b>	<b>3/2007</b>												
690	Migrate from SFC to SFIS for USSGL required elements	3/2006		◆										
691	Implement SFIS Library as single, authoritative source for SFIS values	3/2006		◆										
692	Complete deployments for USSOCOM and Dept. of Army General Fund	3/2006		◆										

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
693	Extend integration between DCW and DDRS for financial statement generation (Army)	3/2006			◆									
694	Army Property, Plant & Equipment (PPE) (Capital Assets)	3/2006			◆									
695	USSOCOM solution for TMA and DARPA	3/2006			◆									
696	Migrate from SFC to SFIS for rest of Phase I elements	9/2006				◆								
697	Analyze level of effort to incorporate SFIS Phase II	9/2006				◆								
698	Centralized Global Edit Table (CGET)	9/2006				◆								
699	USSOCOM solution for MDA, JCS, DSCA, and WHS	9/2006				◆								
700	Additional joint program (Joint Strike Fighter)	9/2006				◆								
701	Extend data processing and "corporate" GL posting capability to Marine Corps	9/2006				◆								
702	Implement SFIS Phase II elements	3/2007					◆							
703	Extend data processing and "corporate" GL posting capability to addition Component (Air Force or Navy)	3/2007					◆							
704	<b>DCD/DCW</b>	<b>3/2006</b>	▨		▨									
705	<b>Key Milestones:</b>	<b>3/2006</b>	▨		▨									
706	Milestone A	5/2000												
707	Milestone B	5/2000												
708	Milestone C	3/2005		◆										
709	IOC	9/2005		◆										
710	FOC	3/2006			◆									
711	<b>DDRS</b>	<b>12/2008</b>	▨		▨		▨		▨					
712	<b>Key Milestones:</b>	<b>12/2008</b>	▨		▨		▨		▨					
713	Milestone A	10/1998												
714	Milestone B	4/2002												
715	Milestone C	9/2003												
716	IOC	10/2003												
717	FOC	3/2006			◆									
718	End convergence	12/2008						◆						
719	<b>Legacy Systems migrating to BEIS</b>	<b>9/2009</b>	▨		▨		▨		▨					
720	DCD/DCW	9/2009												◆
721	<b>DDRS</b>	<b>7/2006</b>			▨	▨								
722	HQARS	12/2005		◆										
723	STARS	7/2006			◆									
724	<b>DCAS</b>	<b>9/2007</b>	▨		▨		▨		▨					
725	<b>Key Milestones:</b>	<b>9/2007</b>	▨		▨		▨		▨					
726	Complete AoA	9/1996												
727	Milestone C	3/2006			◆									
728	IOC	2/2006			◆									
729	FOC	9/2007					◆							
730	Arthur Andersen Study	8/1996												
731	Milestone 0 - (Concept Approved)	5/1998												

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
732	Phase 1 - Cross Disbursing	3/1999												
733	Milestone 1/2 - (Total Program)	5/1999												
734	Milestone 3 - Phase 1 Only	1/2000												
735	Phase 2 - Treasury Reporting (CL/KC)	4/2003												
736	Phase 3 - FRS Elimination	2/2006			◆									
737	Phase 4 - Treasury Reporting (IN/CO)	TBD												
738	Phase 5 - Treasury Reporting (DN)	TBD												
739	Phase 6 - Misc Cash Systems & Reconciliation	TBD												
740	<b>Legacy Systems migrating to DCAS</b>	<b>9/2007</b>												
741	CHOOSE	9/2007					◆							
742	CRS	9/2007					◆							
743	DCMS	9/2007					◆							
744	DFRRS	9/2007					◆							
745	DIT	9/2007					◆							
746	DRO	9/2007					◆							
747	FOS	9/2007					◆							
748	FRS-ACCTG	2/2006			◆									
749	HQARS	3/2006			◆									
750	IBOP	9/2007					◆							
751	MAFR	9/2007					◆							
752	NPPI	9/2007					◆							
753	RECERT	9/2007					◆							
754	SABRS [E&C]	9/2007					◆							
755	SAMS	9/2007					◆							
756	SORS	9/2007					◆							
757	TBO	9/2007					◆							
758	UTP	TBD												
759	WYPC	9/2007					◆							
760	XDISB	9/2007					◆							
761	<b>IGT</b>	<b>10/2005</b>												
762	<b>Key Milestones:</b>	<b>10/2005</b>												
763	<b>Increment: Phase 1</b>	<b>10/2005</b>												
764	Milestone A	12/2004												
765	IOC	10/2005												
766	<b>Key Initiatives</b>	<b>8/2006</b>												
767	<b>PB Framework</b>	<b>8/2006</b>												
768	<b>Key Milestones:</b>	<b>8/2006</b>												
769	<b>Increment: PB Framework Phase I</b>	<b>2/2006</b>												
770	P/B Data Structure links to SFIS	7/2005												
771	Enterprise business rules for PNO	10/2005												
772	Determine authoritative data sources	2/2006												

*Enterprise Transition Plan, Appendix J: System Transition Schedule*

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
773	<b>Increment: PB Framework Phase II</b>	<b>8/2006</b>			▽									
774	P/B Data Structure links to SFIS	5/2006			◆									
775	Determine authoritative data sources	8/2006			◆									
776	<b>SFIS</b>	<b>7/2006</b>			▽									
777	<b>Key Milestones:</b>	<b>7/2006</b>			▽									
778	Initial Policy	7/2005		◆										
779	Phase I Definition: Financial Statement Elements	5/2005		◆										
780	Phase II Definition: Cost/Performance Management Element	1/2006			◆									
781	Phase III Definition: Elements TBD	7/2006			◆									
782														

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	
783	<b>Components</b>	<b>10/2018</b>													
784	<b>Air Force</b>	<b>11/2016</b>													
785	<b>Key Systems</b>	<b>9/2015</b>													
786	<b>ACES</b>	<b>11/2008</b>													
787	<b>Key Milestones:</b>	<b>11/2008</b>													
788	<b>Increment: OPS Modernization</b>	<b>10/2005</b>													
789	FOC	10/2005													
790	<b>Increment: Phase 1 Modernization</b>	<b>11/2007</b>													
791	FOC	11/2007													
792	<b>Increment: Phase 2 Modernization</b>	<b>5/2008</b>													
793	FOC	5/2008													
794	<b>Increment: Phase 3 Modernization</b>	<b>11/2008</b>													
795	FOC	11/2008													
796	<b>Legacy Systems migrating to ACES</b>	<b>6/2006</b>													
797	IWIMS	6/2006													
798	<b>ADLS</b>	<b>7/2004</b>													
799	<b>Key Milestones:</b>	<b>7/2004</b>													
800	IOC	7/2004													
801	<b>AFRISS</b>	<b>11/2007</b>													
802	<b>Key Milestones:</b>	<b>11/2007</b>													
803	Milestone A	8/1998													
804	Milestone B	12/1998													
805	Milestone C	2/1999													
806	IOC	6/1999													
807	FOC	11/2007													
808	<b>DEAMS-AF</b>	<b>9/2010</b>													
809	<b>Key Milestones:</b>	<b>3/2009</b>													
810	<b>Increment: Inc 1 USTRANSCOM</b>	<b>2/2008</b>													
811	Complete AoA	1/2005													
812	Milestone A	4/2005													
813	Milestone B	1/2007													
814	Milestone C	9/2007													
815	IOC	9/2007													
816	FOC	2/2008													
817	<b>Increment: Inc 2 (USAF)</b>	<b>3/2009</b>													
818	Milestone A	1/2007													
819	Milestone B	2/2008													
820	Milestone C	3/2009													
821	IOC	3/2009													
822	<b>Legacy Systems migrating to DEAMS</b>	<b>9/2010</b>													
823	ABSS	3/2009													

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	
824	ASIFICS	10/2006			◆										
825	BARS	9/2010							◆						
826	CPAS	12/2004	◆												
827	FMS	9/2007				◆									
828	GAFS	9/2010							◆						
829	GAFS-R	9/2010							◆						
830	IAPS	9/2010							◆						
831	TFMS-M	9/2007				◆									
832	<b>EBS</b>	<b>9/2008</b>	◆												
833	<b>Key Milestones:</b>	<b>9/2008</b>	◆												
834	Milestone A	9/1999	◆												
835	Milestone B	2/2000	◆												
836	Milestone C	10/2002	◆												
837	IOC	4/2004	◆												
838	Establish EDM Infrastructure	7/2005		◆											
839	CWE Rollout to AFRL	2/2006			◆										
840	Enterprise Planning & Pgming Syst	8/2006				◆									
841	COTS S&T Project Portfolio Mgt Syst	2/2007					◆								
842	FOC	9/2008						◆							
843	<b>Legacy systems migrating to EBS</b>	<b>3/2007</b>	◆												
844	Agreements	3/2007				◆									
845	APDP Tracking	1/2007				◆									
846	C2S2	1/2007				◆									
847	DiDS	3/2007				◆									
848	DTTIS	10/2006				◆									
849	G2	1/2007				◆									
850	HE-PERS	1/2007				◆									
851	HQ P&P	2/2006			◆										
852	HR2K	1/2007				◆									
853	HR-DEVS	1/2007				◆									
854	HWIS	3/2007				◆									
855	IR&D	8/2005		◆											
856	Jiffy	3/2007				◆									
857	LMS	1/2007				◆									
858	Mentoring	1/2007				◆									
859	Oz-SPA	3/2007				◆									
860	PA Database	3/2007				◆									
861	PR-w Contrak	3/2007				◆									
862	PTI	8/2005		◆											
863	RCDB	2/2006			◆										
864	Tech Connect	8/2005		◆											

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
865	Vocus	8/2005		◆										
866	Warfighter	2/2006			◆									
867	Web Project Room	3/2007				◆								
868	WURMS	3/2007				◆								
869	<b>ECSS-IL</b>	<b>9/2013</b>												
870	<b>Key Milestones:</b>	<b>9/2012</b>												
871	Milestone A	8/2005		◆										
872	Milestone B	12/2007				◆								
873	Milestone C	10/2008					◆							
874	IOC	3/2011								◆				
875	FOC	9/2012									◆			
876	<b>Legacy Systems migrating to ECSS-IL</b>	<b>9/2013</b>												
877	A&S	9/2010								◆				
878	ABS	9/2010								◆				
879	AFEMS	9/2010								◆				
880	AFERS	9/2011									◆			
881	AFPS	9/2011									◆			
882	AIRCAT	9/2013										◆		
883	ALMSS	9/2011									◆			
884	ALSDS(E046BREFRESH)	9/2011									◆			
885	AMMO-WEB	9/2010								◆				
886	API	9/2010								◆				
887	APS	9/2009									◆			
888	ASMS	9/2011									◆			
889	ASSAT	9/2009									◆			
890	ATOMS	9/2010								◆				
891	ATOS	9/2010								◆				
892	BASES	9/2011									◆			
893	BITS IBRC	9/2011									◆			
894	C2Remedy	9/2010								◆				
895	CAMS-FM/G081	9/2011									◆			
896	CANS	9/2011									◆			
897	CARS	9/2013										◆		
898	CAS	9/2011									◆			
899	CAS 1.0	9/2011									◆			
900	CAS-A	9/2010								◆				
901	CCS	9/2011									◆			
902	CD	9/2008					◆							
903	CEMS	9/2011									◆			
904	CERC	9/2009								◆				
905	CIDS	9/2010								◆				

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
906	CITOMS	9/2010							◆					
907	CMOS	9/2010							◆					
908	COINS	9/2010							◆					
909	COPA	9/2009						◆						
910	CPPM	9/2010							◆					
911	CSIS	9/2010							◆					
912	DMAPS	9/2013										◆		
913	DMCODB	9/2011								◆				
914	DMMSS	9/2010							◆					
915	DMSI	9/2011								◆				
916	DRIS	9/2010							◆					
917	EIP(D200C)	9/2010							◆					
918	EMOC	9/2013										◆		
919	EPS	9/2011								◆				
920	EXPRESS	9/2011								◆				
921	FAS	9/2010							◆					
922	FEM	9/2011								◆				
923	FIABS	9/2010							◆					
924	Form196	9/2010							◆					
925	FSS	9/2010							◆					
926	GFMR	9/2010							◆					
927	GIMMS	9/2011								◆				
928	HMMS	9/2010							◆					
929	I&SSS	9/2010							◆					
930	ICBM MDC	9/2010							◆					
931	ICS	9/2010							◆					
932	IDIM	9/2010							◆					
933	IES	9/2011								◆				
934	IIMS	9/2011								◆				
935	ILDS	9/2010							◆					
936	ILS-S	9/2011								◆				
937	IMACS	9/2011								◆				
938	IMCS	9/2010							◆					
939	IMDB	9/2013										◆		
940	IMDS-IL	9/2011								◆				
941	IMMP	9/2009						◆						
942	IMWRP	9/2011								◆				
943	INSTOR	9/2010							◆					
944	IRD	9/2009						◆						
945	ITS (2)	9/2011								◆				
946	JOPMS	9/2011								◆				

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
947	KDSS	9/2013										◆		
948	LDM	9/2013										◆		
949	LDMS	9/2011												
950	LIAMS (WAS OLVIMS)	9/2011										◆		
951	LMDS	9/2010							◆			◆		
952	MABSM	9/2011										◆		
953	Material	9/2013										◆		
954	MCIP(D035W)	9/2011										◆		
955	MCPS	9/2011										◆		
956	MERLIN	9/2013										◆		
957	MFRS	9/2010							◆					
958	MICAP	9/2011										◆		
959	MICAS	9/2010							◆					
960	MIICS	9/2010							◆					
961	MIIDB	9/2010							◆					
962	MISTR	9/2011										◆		
963	MPE	9/2011										◆		
964	MPS	9/2011										◆		
965	MRDCS	9/2011										◆		
966	MWAS	9/2010							◆					
967	MWMS	9/2009						◆						
968	MWPCS	9/2011										◆		
969	Ogden PDMSS WEB	9/2011										◆		
970	ORA	9/2013										◆		
971	OWRMR	9/2009						◆						
972	PACSS/QIMSS	9/2011										◆		
973	PADS	9/2013										◆		
974	PAMS	9/2008					◆							
975	PCMS (2)	9/2011										◆		
976	PDMSS	9/2011										◆		
977	PDMSS WEB	9/2011										◆		
978	PIECS	9/2010							◆					
979	POMX	9/2011										◆		
980	PPAS	9/2011										◆		
981	PRPS - AFMC	9/2010							◆					
982	PRS	9/2011										◆		
983	PWPS	9/2011										◆		
984	RAM	9/2011										◆		
985	RAM/TMRS	9/2013										◆		
986	RAMP	9/2011										◆		
987	RAMPOD	9/2011										◆		

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
988	RCAS	9/2011								◆				
989	REALM G	9/2011								◆				
990	REALM H	9/2010							◆					
991	REMIS	9/2013										◆		
992	RFM	9/2009						◆						
993	RIID	9/2010							◆					
994	RIS	9/2009						◆						
995	RMS	9/2010							◆					
996	RSSL	9/2010							◆					
997	RSSP DE	9/2009						◆						
998	SACS	9/2010							◆					
999	SAM	9/2011								◆				
1000	SAMS	9/2013										◆		
1001	SATODS(W002)	9/2010							◆					
1002	SATS	9/2010							◆					
1003	SAV	9/2011								◆				
1004	SBSS/ILS-S	9/2011								◆				
1005	SCCOP	9/2010							◆					
1006	SCS	9/2011								◆				
1007	SIRS	9/2009						◆						
1008	SIS	9/2010							◆					
1009	SNUD	9/2011								◆				
1010	SSRAC	9/2011								◆				
1011	SSSC	9/2010							◆					
1012	TABBS	9/2009						◆						
1013	TAS	9/2008					◆							
1014	TF39 CWA	9/2013										◆		
1015	TRACKER	9/2010							◆					
1016	TSC	9/2011								◆				
1017	WAPDS	9/2009						◆						
1018	WARRS	9/2010							◆					
1019	WMER	9/2008					◆							
1020	WR CTOR	9/2010							◆					
1021	WSMIS	9/2011								◆				
1022	<b>EESOH-MIS</b>	<b>12/2007</b>												
1023	<b>Key Milestones:</b>	<b>1/2007</b>												
1024	<b>Version 1.1 (Hazmat)</b>	<b>6/2005</b>		◆										
1025	FOC	6/2005		◆										
1026	<b>Version 1.2 (Cleanup)</b>	<b>12/2005</b>			◆									
1027	FOC	12/2005			◆									
1028	<b>Version 1.3 (HazWaste)</b>	<b>9/2006</b>				◆								

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1029	FOC	9/2006			◆									
1030	<b>Version 1.4 (Air) APIMS Rpl</b>	<b>1/2007</b>			◆									
1031	FOC	1/2007			◆									
1032	<b>Legacy Systems migrating to EESOH-MIS</b>	<b>12/2007</b>			▾	▾								
1033	AF-EMIS	12/2006			◆									
1034	AFRIMS	3/2006			◆									
1035	AirCop	11/2006			◆									
1036	APIMS	11/2006			◆									
1037	AQUTS	11/2006			◆									
1038	ENTRAC	12/2007					◆							
1039	HAZCOM	9/2006			◆									
1040	HMMS (AF Use)	9/2007				◆								
1041	HOMER	9/2007				◆								
1042	SMART	12/2006			◆									
1043	WITS	9/2007				◆								
1044	<b>ETIMS</b>	<b>3/2010</b>			▾	▾	▾	▾						
1045	<b>Key Milestones:</b>	<b>3/2010</b>			▾	▾	▾	▾						
1046	<b>Increment: Spiral 1</b>	<b>10/2006</b>			▾	▾								
1047	Complete AoA	6/2005		◆										
1048	Milestone B	11/2005		◆										
1049	Milestone C	4/2006			◆									
1050	IOC	4/2006			◆									
1051	Deploy Spiral 1	10/2006			◆									
1052	<b>Increment: Spiral 2</b>	<b>10/2008</b>					▾	▾						
1053	Spiral 2 requirements and design	2/2007				◆								
1054	Spiral 2 development, test, and development	10/2008					◆							
1055	<b>Increment: Spiral 3</b>	<b>3/2010</b>						▾	▾					
1056	Spiral 3 requirements and design	6/2008					◆							
1057	FOC	9/2009						◆						
1058	Spiral 3 development, test, and deployment	9/2009						◆						
1059	Sustainment	3/2010							◆					
1060	<b>Legacy Systems migrating to ETMS</b>	<b>9/2009</b>			▾	▾	▾	▾						
1061	AFTOX	10/2006			◆									
1062	ATIMS	10/2008					◆							
1063	ATOMS	10/2006			◆									
1064	ATOS/DLDSS	9/2009						◆						
1065	CARDFILE	10/2008					◆							
1066	CTOR	10/2008					◆							
1067	E847	10/2006			◆									
1068	ETOMS	10/2008					◆							
1069	GEORGE	9/2009						◆						

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1070	IDM	9/2009						◆						
1071	IDTOD	9/2009						◆						
1072	JCALs	10/2008					◆							
1073	LDBMS	10/2006			◆									
1074	LIMITS	10/2008					◆							
1075	PTOWS	9/2009						◆						
1076	SATODS	9/2009						◆						
1077	TDMS	10/2008					◆							
1078	TODS	10/2008					◆							
1079	TOMART	10/2006			◆									
1080	TOMCOP	10/2006			◆									
1081	<b>FIRST</b>	<b>9/2011</b>	◆											
1082	<b>Key Milestones:</b>	<b>9/2010</b>	◆											
1083	Milestone B	3/2001												
1084	Milestone C	5/2007				◆								
1085	IOC	9/2007				◆								
1086	FOC	9/2010							◆					
1087	<b>Legacy Systems migrating to FIRST</b>	<b>9/2011</b>	◆											
1088	ABIDES	3/2009						◆						
1089	ABSS	7/2008					◆							
1090	CBAS II	5/2006			◆									
1091	CMS	3/2007				◆								
1092	MicroBAS	12/2005		◆										
1093	OARS	9/2011								◆				
1094	PBAS	12/2005		◆										
1095	<b>MPES-DP</b>	<b>5/2005</b>	◆											
1096	<b>Key Milestones:</b>	<b>5/2005</b>	◆											
1097	FOC	5/2005	◆											
1098	<b>Legacy systems migrating to MPES-DP</b>	<b>4/2005</b>	◆											
1099	MDS	4/2005	◆											
1100	<b>NAF-T</b>	<b>9/2015</b>	◆											
1101	<b>Key Milestones:</b>	<b>9/2015</b>	◆											
1102	<b>Increment: Phase 1-Financial</b>	<b>10/2008</b>	◆											
1103	Complete AoA	6/2002												
1104	Business case	6/2002												
1105	Enterprise-wide domain architecture study	6/2003												
1106	Enterprise Portfolio Management	9/2003												
1107	Milestone A	12/2003												
1108	Acquisition of COTS Solution	3/2004	◆											
1109	Stand up of Shared Service Center	7/2004	◆											
1110	Transition Plan	6/2004	◆											

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1111	Milestone B	3/2005		◆										
1112	Milestone C	6/2005		◆										
1113	Interface current standard AF Services POS systems to COTS	9/2005		◆										
1114	Interface with DCPDS	9/2005		◆										
1115	Interface with IBPS	9/2005		◆										
1116	Business Process Re-engineering	10/2005		◆										
1117	Initial Policy	12/2005		◆										
1118	IOC	12/2005		◆										
1119	Shared Service Center Fully Operational	2/2008					◆							
1120	FOC	9/2008					◆							
1121	Final Policy Implemented	9/2008					◆							
1122	Agile Combat Support	10/2008					◆							
1123	Global Services	10/2008					◆							
1124	Informed Decision-Making Capabilities	10/2008					◆							
1125	Lean business/information processing	10/2008					◆							
1126	<b>Increment: Phase 2-POS Modernization</b>	<b>9/2010</b>			◆									
1127	Milestone C	6/2005		◆										
1128	Business case	9/2006			◆									
1129	Initial Policy	3/2007				◆								
1130	Business Process Re-engineering	3/2007				◆								
1131	Enterprise-wide domain architecture study	3/2007				◆								
1132	Transition Plan	6/2007				◆								
1133	FOC	9/2010							◆					
1134	Agile Combat Support	9/2010							◆					
1135	Final Policy Implemented	9/2010							◆					
1136	Global Services	9/2010							◆					
1137	Informed Decision-Making Capabilities	9/2010							◆					
1138	Lean business/information processing	9/2010							◆					
1139	Enterprise Portfolio Management	9/2010							◆					
1140	<b>Increment: Phase 3-Supply Chain Mgmt</b>	<b>9/2015</b>			◆									
1141	Business case	9/2006			◆									
1142	Enterprise-wide domain architecture study	3/2007				◆								
1143	Business Process Re-engineering	9/2009						◆						
1144	Transition Plan	6/2009						◆						
1145	Initial Policy	9/2009						◆						
1146	Global Services	9/2015												◆
1147	Informed Decision-Making Capabilities	9/2015												◆
1148	Lean business/information processing	9/2015												◆
1149	Enterprise Portfolio Management	9/2015												◆
1150	Agile Combat Support	9/2015												◆
1151	FOC	9/2015												◆

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1152	Final Policy Implemented	9/2015												◆
1153	<b>Increment: Phase 4-CRM</b>	<b>9/2015</b>			▶									
1154	Transition Plan	6/2006			◆									
1155	Business case	9/2006			◆									
1156	Enterprise-wide domain architecture study	3/2007				◆								
1157	Initial Policy	9/2010								◆				
1158	Business Process Re-engineering	9/2010								◆				
1159	FOC	9/2015												◆
1160	Final Policy Implemented	9/2015												◆
1161	Agile Combat Support	9/2015												◆
1162	Enterprise Portfolio Management	9/2015												◆
1163	Global Services	9/2015												◆
1164	Informed Decision-Making Capabilities	9/2015												◆
1165	Lean business/information processing	9/2015												◆
1166	<b>Legacy Systems migrating to NAF-T</b>	<b>11/2008</b>						◆						
1167	NAFMIS	11/2008						◆						
1168	FAS	11/2008						◆						
1169	<b>Key Initiatives</b>	<b>11/2016</b>	▶											
1170	<b>AFIR&amp;I</b>	<b>11/2016</b>								▶	▶	▶	▶	▶
1171	<b>Key Milestones:</b>	<b>11/2016</b>								▶	▶	▶	▶	▶
1172	<b>Increment: Increment 1</b>	<b>7/2013</b>								▶	▶	▶	▶	▶
1173	Maintain Reliable Budgetary Accounting Information to Support an Unqualified Audit Opinion on the Statement of Budgetary Resources. (Incr 1): Request Internal Validation;(Incr 2): Air Force Management Assertion to OSD/IG; (Incr 3): Audit Opinion Received	7/2010								◆				
1174	Maintain Reliable Cost Information for Air Force Programs to Support an Unqualified Audit Opinion on the Statement of Net Cost. (Increment 1): Request Internal Validation; (Increment 2): Air Force Management Assertion to OSD/IG; (Increment 3):	7/2013										◆		
1175	Maintain Reliable Information for all Air Force Assets and Liabilities to Support an Unqualified Audit Opinion on the Balance Sheet. (Incr 1): Request Internal Validation; (Incr 2): Air Force Management Assertion to OSD/IG; (Incr 3) Audit Opinion Received	7/2013										◆		
1176	<b>Increment: Increment 2</b>	<b>4/2014</b>								▶	▶	▶	▶	▶
1177	Maintain Reliable Budgetary Accounting Information to Support an Unqualified Audit Opinion on the Statement of Budgetary Resources.(Incr 1): Request Internal Validation; (Incr 2): Air Force Management Assertion to OSD/IG; (Incr 3): Audit Opinion Received	4/2011								◆				

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1178	Maintain Reliable Cost Information for Air Force Programs to Support an Unqualified Audit Opinion on the Statement of Net Cost. (Increment 1): Request Internal Validation; (Increment 2): Air Force Management Assertion to OSD/IG; (Increment 3):	4/2014											◆	
1179	Maintain Reliable Information for all Air Force Assets and Liabilities to Support an Unqualified Audit Opinion on the Balance Sheet. (Incr 1): Request Internal Validation; (Incr 2): Air Force Management Assertion to OSD/IG; (Incr 3) Audit Opinion Received	4/2014											◆	
1180	<b>Increment: Increment 3</b>	<b>11/2016</b>											▨	
1181	Maintain Reliable Budgetary Accounting Information to Support an Unqualified Audit Opinion on the Statement of Budgetary Resources.(Incr 1): Request Internal Validation; (Incr 2): Air Force Management Assertion to OSD/IG; (Incr 3): Audit Opinion Received	11/2013										◆		
1182	Maintain Reliable Cost Information for Air Force Programs to Support an Unqualified Audit Opinion on the Statement of Net Cost. (Increment 1): Request Internal Validation; (Increment 2): Air Force Management Assertion to OSD/IG; (Increment 3):	11/2016												
1183	Maintain Reliable Information for all Air Force Assets and Liabilities to Support an Unqualified Audit Opinion on the Balance Sheet. (Incr 1): Request Internal Validation; (Incr 2): Air Force Management Assertion to OSD/IG; (Incr 3) Audit Opinion Received	11/2016												
1184	<b>ELR</b>	<b>5/2008</b>	▨											
1185	<b>Key Milestones:</b>	<b>5/2008</b>	▨											
1186	<b>Increment: OS Command and Control</b>	<b>12/2007</b>	▨											
1187	Value Stream Analysis	12/2004		◆										
1188	ID critical processes	4/2004	◆											
1189	Implement improvements incrementally, AF-wide	6/2005		◆										
1190	Initiate RIEs	5/2005		◆										
1191	Complete RIEs	4/2007				◆								
1192	Complete AF-wide incremental changes	12/2007					◆							
1193	<b>Increment: Deployment Management</b>	<b>6/2007</b>	▨											
1194	ID critical processes	4/2004	◆											
1195	Value Stream Analysis	6/2004	◆											
1196	Initiate RIEs	11/2004		◆										
1197	Implement improvements incrementally, AF-wide	12/2004		◆										
1198	Complete RIEs	10/2006				◆								
1199	Complete AF-wide incremental changes	6/2007					◆							
1200	<b>Increment: Full Spectrum Threat Response</b>	<b>5/2007</b>	▨											
1201	ID critical processes	4/2004	◆											
1202	Value Stream Analysis	11/2004		◆										
1203	Initiate RIEs	4/2005		◆										

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1204	Implement improvements incrementally, AF-wide	5/2005		◆										
1205	Complete RIEs	3/2007				◆								
1206	Complete AF-wide incremental changes	5/2007				◆								
1207	<b>Increment: Spiral 2 OS 5 Critical Processes for Re-engineering</b>	<b>5/2008</b>			▬									
1208	ID critical processes	10/2005		◆										
1209	Value Stream Analysis	11/2005		◆										
1210	Initiate RIEs	3/2006			◆									
1211	Implement improvements incrementally, AF-wide	5/2006			◆									
1212	Complete AF-wide incremental changes	5/2008					◆							
1213	Complete RIEs	2/2008					◆							
1214	<b>FM SDM</b>	<b>9/2009</b>			▬									
1215	<b>Key Milestones:</b>	<b>9/2009</b>			▬									
1216	Center of Expertise IOC	10/2005		◆										
1217	Financial Advisor Transformation: Realign ALO/FMA	12/2005		◆										
1218	Financial Services Transformation: Stand-up Central Processing Center	10/2007				◆								
1219	FAT: Enhanced Financial Advisor. Note Pending DEAMS and Senior Leader approval	9/2008					◆							
1220	Center of Expertise FOC	9/2008					◆							
1221	FST: Stand-up Contact Center	10/2008					◆							
1222	Combat Comptroller Contingency Organization FOC	9/2009						◆						
1223	<b>OSMP</b>	<b>4/2007</b>			▬									
1224	<b>Key Milestones:</b>	<b>4/2007</b>			▬									
1225	Governance	2/2004	◆											
1226	Process direction	5/2004	◆											
1227	CONOPS Definition	5/2004	◆											
1228	OS Enterprise Architecture V3	4/2005		◆										
1229	Enterprise Strategy	5/2005		◆										
1230	Enterprise Portfolio Mgmt	10/2005		◆										
1231	Change Mgmt Plan / Communications	12/2005			◆									
1232	CONOPS Integration	3/2006			◆									
1233	Enterprise Transfo Metrics	3/2006			◆									
1234	Integrated VSA	4/2006			◆									
1235	Integrated AF Transformation	10/2006				◆								
1236	Capabilities based transfo budgeting	3/2007				◆								
1237	Doctrine Integration	3/2007				◆								
1238	Int. Re-Engineering + I-CRRA	4/2007				◆								
1239	Integrated Architecture V5	4/2007				◆								
1240	<b>Pers Trans</b>	<b>9/2006</b>			▬									
1241	<b>Key Milestones:</b>	<b>9/2006</b>			▬									
1242	<b>Increment: AF Military Uniques to DIMHRS</b>	<b>9/2006</b>			▬									

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1243	Consolidated Contact Center-Spiral 1	3/2006			◆									
1244	Milestone B	3/2006			◆									
1245	Consolidated Contact Center-Spiral 2	6/2006			◆									
1246	Consolidated Contact Center-Spiral 3	9/2006			◆									
1247	<b>Increment: AF Civilian Uniques to DCPDS</b>	<b>8/2004</b>	◀											
1248	IOC	3/2002												
1249	FOC	8/2004	◆											
1250	<b>Increment: Military Personnel Data System</b>	<b>7/2001</b>												
1251	IOC	6/2001												
1252	FOC	7/2001												
1253	<b>PM&amp;O</b>	<b>12/2008</b>												
1254	<b>Key Milestones:</b>	<b>12/2008</b>												
1255	IRSS on NIPRNET (GCSS)	7/2005		◆										
1256	IRSS AFROCC, JROC Integration	3/2006			◆									
1257	SMART data feed to DAMIR	12/2006				◆								
1258	SMART/CCaR/IDECs linked	12/2007					◆							
1259	SMART evolved to Acq Portal	12/2008						◆						
1260	PRIDE functionality to the Portal	12/2008						◆						
1261	<b>Sourcing</b>	<b>12/2007</b>												
1262	<b>Key Milestones:</b>	<b>12/2007</b>												
1263	CARS (J001) replaced by FPDS-NG	10/2005		◆										
1264	AFWAY upgrade to AFEBuy	8/2006			◆									
1265	ACPS replaced by SPS V 4.2.3	3/2007				◆								
1266	ConWrite replaced by SPS V 4.2.3	12/2007					◆							
1267	<b>T&amp;E</b>	<b>8/2005</b>		◆										
1268	<b>Key Milestones:</b>	<b>8/2005</b>		◆										
1269	AFMC selection of preferred modules	8/2005		◆										
1270														
1271	<b>Army</b>	<b>10/2018</b>												
1272	<b>Key Systems</b>	<b>10/2018</b>												
1273	<b>ACBIS</b>	<b>1/2005</b>												
1274	<b>Key Milestones:</b>	<b>1/2005</b>												
1275	<b>Increment: Block One</b>	<b>10/2003</b>												
1276	Milestone A	8/2002												
1277	IOC	4/2003												
1278	FOC	10/2003												
1279	<b>Increment: Block Two</b>	<b>10/2004</b>	◀											
1280	IOC	5/2004	◆											
1281	FOC	10/2004		◆										
1282	<b>Increment: Block Three</b>	<b>1/2005</b>		◆										
1283	IOC	1/2005		◆										

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	
1284	<b>AIM</b>	<b>9/2018</b>													
1285	<b>Key Milestones:</b>	<b>9/2018</b>													
1286	<b>Increment: AIM 7.0</b>	<b>9/2005</b>													
1287	Requirements	3/2005		◆											
1288	Design	5/2005		◆											
1289	Development	7/2005		◆											
1290	Testing	8/2005		◆											
1291	Fielding	9/2005		◆											
1292	<b>Increment: AIM 8.0</b>	<b>3/2006</b>													
1293	Requirements	9/2005		◆											
1294	Fielding	3/2006		◆											
1295	<b>Increment: AIM 9.0</b>	<b>9/2006</b>													
1296	Requirements	3/2006		◆											
1297	Fielding	9/2006		◆											
1298	<b>Increment: AIM 10.0</b>	<b>9/2008</b>					◆								
1299	Fielding	9/2008					◆								
1300	<b>Increment: Firedog Evolution</b>	<b>9/2018</b>													
1301	Acq Domain Support (Firedog)	9/2018													
1302	<b>DLS</b>	<b>9/2010</b>													
1303	<b>Key Milestones:</b>	<b>9/2010</b>													
1304	<b>Increment 1 - Digital Training Facilities</b>	<b>3/1999</b>													
1305	Milestone A	4/1998													
1306	Milestone B	4/1998													
1307	Milestone C	3/1999													
1308	<b>Increment 2 - Subsume Increment 1 with Updated Digital Training Facilities and DLS Enterprise Management</b>	<b>9/2005</b>													
1309	Milestone A	3/1999													
1310	Milestone B	3/1999													
1311	IOC	12/1999													
1312	Milestone C	12/2000													
1313	FOC	9/2005		◆											
1314	<b>Increment 3 - Army Learning Management System</b>	<b>12/2007</b>													
1315	Milestone A	12/2000													
1316	Milestone B	12/2000													
1317	Milestone C	9/2004		◆											
1318	IOC	12/2004		◆											
1319	FOC	12/2007					◆								
1320	<b>Increment 4 - Deployed Digital Training Campus</b>	<b>9/2010</b>													
1321	Milestone A	9/2004		◆											
1322	Milestone B	9/2004		◆											
1323	Milestone C	12/2007					◆								
1324	IOC	6/2007				◆									

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1325	Requirements Analysis	6/2005		◆										
1326	Contract Award	4/2006			◆									
1327	SDD	7/2006			◆									
1328	DT&E	1/2007				◆								
1329	OT&E	7/2007				◆								
1330	FRP	12/2007					◆							
1331	Fielding	1/2008					◆							
1332	FOC	9/2010							◆					
1333	<b>Legacy systems migrating to DLS</b>	<b>12/2007</b>					◆							
1334	AIMS-PC	12/2007					◆							
1335	TREDS-R	12/2007					◆							
1336	<b>eMILPO</b>	<b>8/2003</b>												
1337	<b>Key Milestones:</b>	<b>8/2003</b>												
1338	FOC	8/2003												
1339	<b>FBS</b>	<b>10/2018</b>												
1340	<b>Key Milestones:</b>	<b>10/2018</b>												
1341	<b>Increment: Increment 1</b>	<b>1/2014</b>												
1342	Develop BCA and POM Requirements	4/2004	◆											
1343	Establish Army FBS Governance Organization and Processes	6/2005		◆										
1344	Milestone A	12/2005		◆										
1345	Army FBS enable 3 key Communities of Interest	8/2006			◆									
1346	Technology Prototyping and Component Integration Readiness and Benefits Assessments	12/2006			◆									
1347	Milestone B	4/2007				◆								
1348	Develop Reference Architecture	4/2007				◆								
1349	Evaluation of Candidate Applications	10/2007				◆								
1350	Milestone C	6/2008					◆							
1351	IOC	1/2009						◆						
1352	FOC	1/2014											◆	
1353	<b>Increment: Increment 2</b>	<b>1/2010</b>												
1354	Milestone B	6/2008					◆							
1355	Milestone C	6/2009						◆						
1356	IOC	1/2010							◆					
1357	<b>Increment: Increment 3</b>	<b>1/2011</b>												
1358	Milestone B	6/2009						◆						
1359	Milestone C	6/2010							◆					
1360	IOC	1/2011								◆				
1361	<b>Increment: Increment 4</b>	<b>1/2012</b>												
1362	Milestone B	6/2010							◆					
1363	Milestone C	6/2011								◆				
1364	IOC	1/2012									◆			

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1365	<b>Increment: Implement 5</b>	<b>10/2018</b>												
1366	Milestone B	6/2011								◆				
1367	Milestone C	6/2012									◆			
1368	IOC	1/2013										◆		
1369	Produce and Deploy 13 FBS enabled Remaining COIs	9/2013											◆	
1370	Evolve and sustain 16 COIs	10/2018												
1371	<b>Legacy systems migrating to FBS</b>	<b>6/2013</b>												
1372	ACBIS	6/2012												
1373	ACE	TBD												
1374	AIM	6/2011								◆				
1375	STEM	6/2013										◆		
1376	VIS	6/2011								◆				
1377	VISION	6/2012									◆			
1378	<b>FCS-ACE</b>	<b>10/2005</b>												
1379	<b>Key Milestones:</b>	<b>10/2005</b>												
1380	Contract Award (Initial Production)	5/2003												
1381	Milestone B	5/2003												
1382	Blockpoint 1-17: Capabilities deployed with FCS ACE to support FCS program. (Inc. 1 commenced 05/2003)	2/2005		◆										
1383	Blockpoint 18: Capabilities deployed for FCS IPR2	3/2005		◆										
1384	Blockpoint 19	4/2005		◆										
1385	Blockpoint 20	6/2005		◆										
1386	Blockpoint 21: Capabilities deployed for FCS SoSFR	8/2005		◆										
1387	Blockpoint 22	10/2005		◆										
1388	<b>GCSS-A</b>	<b>4/2010</b>												
1389	<b>Key Milestones:</b>	<b>3/2010</b>												
1390	<b>Increment 1--Implement ORD Block 1 functionality and interface hub to external systems.</b>	<b>3/2010</b>												
1391	MS 0/I/II (MAISRC) decision	5/1997												
1392	ACAT 1D designation	5/2002												
1393	Complete AoA	3/2003												
1394	Milestone B	12/2005		◆										
1395	Milestone C	8/2007				◆								
1396	IOC	9/2007				◆								
1397	FOC	3/2010								◆				
1398	<b>Legacy Systems migrating to GCSS-A</b>	<b>4/2010</b>								◆				
1399	PBUSE	4/2010								◆				
1400	SAAS-MOD	4/2010								◆				
1401	SAMS-1 Rehost	4/2010								◆				
1402	SARSS 1(I)	4/2010								◆				
1403	SARSS-2AC/2B	4/2010								◆				
1404	SARSS-2AD	4/2010								◆				

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1405	SPBS-R	4/2010							◆					
1406	ULLS-A	4/2010							◆					
1407	ULLS-G	4/2010							◆					
1408	ULLS-S4	4/2010							◆					
1409	<b>GFEBS</b>	<b>6/2010</b>												
1410	<b>Key Milestones:</b>	<b>4/2010</b>												
1411	Complete AoA	10/2004	◆											
1412	Milestone A	6/2005		◆										
1413	Milestone B	1/2007				◆								
1414	IOC	11/2007					◆							
1415	Milestone C	6/2008						◆						
1416	Milestone B2	10/2008							◆					
1417	Milestone C2	2/2009								◆				
1418	FOC	4/2010												
1419	<b>Legacy Systems migrating to GFEBS</b>	<b>6/2010</b>												
1420	AORS	6/2010							◆					
1421	ARCS	6/2010							◆					
1422	ASK-FM	6/2010							◆					
1423	ATLAS	6/2010							◆					
1424	AVPRAT	6/2010							◆					
1425	CAMS-ME	6/2010							◆					
1426	CAPS	6/2010							◆					
1427	CRP	6/2010							◆					
1428	DARS	6/2010							◆					
1429	DbCAS/ WebCAS	6/2010							◆					
1430	DJAS	6/2010							◆					
1431	Fadtool	6/2010							◆					
1432	FMIS MEDCOM	6/2010							◆					
1433	GTS	6/2010							◆					
1434	IPAC Wizard	6/2010							◆					
1435	ISB	6/2010							◆					
1436	MS Access data conversion database	6/2010							◆					
1437	ODS	6/2010							◆					
1438	OLRV	6/2010							◆					
1439	On-Base	6/2010							◆					
1440	ONE-PAY	6/2010							◆					
1441	PARSS	6/2010							◆					
1442	RSBUX	6/2010							◆					
1443	SCRT	6/2010							◆					
1444	SLAD	6/2010							◆					
1445	SOMARDS	6/2010							◆					

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1446	STANFINS	6/2010							◆					
1447	VPIS	6/2010							◆					
1448	<b>LMP</b>	<b>7/2007</b>				▬								
1449	<b>Key Milestones:</b>	<b>7/2007</b>				▬								
1450	Complete Financial Management Review	5/2006			◆									
1451	2d Deployment Go Live	7/2006			◆									
1452	3d Deployment Go Live	7/2007				◆								
1453	<b>Legacy Systems migrating to LMP</b>	<b>7/2007</b>				◆								
1454	CCSS	7/2007				◆								
1455	SDS	7/2007				◆								
1456	<b>RCAS</b>	<b>10/2004</b>	▬											
1457	<b>Key Milestones:</b>	<b>10/2004</b>	▬											
1458	<b>Increment: RCAS Solution</b>	<b>10/2004</b>	▬											
1459	Complete AoA	9/1995												
1460	Milestone A	9/1996												
1461	Milestone B	1/1998												
1462	Milestone C	5/2000												
1463	IOC	7/2001												
1464	Milestone E	3/2002												
1465	Milestone F	3/2003												
1466	FOC	10/2004	◆											
1467	Milestone G	10/2004	◆											
1468	<b>STEM</b>	<b>6/2008</b>	▬											
1469	<b>Key Milestones:</b>	<b>2/2006</b>	▬											
1470	<b>Increment: v1.0</b>	<b>2/2005</b>	▬											
1471	First STEM release	2/2005			◆									
1472	Final Policy Implemented	6/2004	◆											
1473	<b>Increment: Enhancements/Upgrades</b>	<b>8/2005</b>			◆									
1474	Financials	8/2005			◆									
1475	Tasker management	8/2005			◆									
1476	<b>Increment: v2.0</b>	<b>2/2006</b>			◆									
1477	version 2.0	2/2006			◆									
1478	<b>Legacy Systems migrating to STEM</b>	<b>6/2008</b>					◆							
1479	ASTMIS	6/2008					◆							
1480	<b>TC-AIMS II</b>	<b>10/2011</b>	▬											
1481	<b>Key Milestones:</b>	<b>10/2011</b>	▬											
1482	<b>Increment: Block 1</b>	<b>5/2004</b>	▬											
1483	Complete AoA	1/1996												
1484	Milestone B	10/2000												
1485	Milestone C	11/2002												
1486	IOC	2/2003												

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1487	FOC	5/2004	◆											
1488	<b>Increment: Block 2</b>	<b>12/2005</b>		▬										
1489	Complete AoA	12/2003												
1490	Milestone B	3/2002												
1491	Milestone C	5/2004	◆											
1492	IOC	8/2004	◆											
1493	FOC	12/2005			◆									
1494	<b>Increment: Block 3</b>	<b>3/2008</b>					▬							
1495	Milestone B	5/2004	◆											
1496	Milestone C	12/2005			◆									
1497	IOC	3/2006			◆									
1498	FOC	3/2008					◆							
1499	<b>Increment: Block 4</b>	<b>3/2010</b>						▬						
1500	Milestone B	12/2005			◆									
1501	Milestone C	3/2008					◆							
1502	IOC	6/2008					◆							
1503	FOC	3/2010							◆					
1504	<b>Increment: Block 5</b>	<b>9/2010</b>						▬						
1505	Milestone B	3/2008					◆							
1506	Milestone C	3/2010							◆					
1507	IOC	6/2010							◆					
1508	FOC	9/2010								◆				
1509	<b>Legacy Systems migrating to TC-AIMS II</b>	<b>10/2011</b>								▬				
1510	CMOS	10/2011									◆			
1511	TC-ACCIS	10/2003												
1512	TC-AIMS	10/2009							◆					
1513	TIS-TO	11/2006				◆								
1514	<b>VIS</b>	<b>10/2005</b>		▬										
1515	<b>Key Milestones:</b>	<b>10/2005</b>		▬										
1516	<b>Increment: Phase 1 Limited Deployment</b>	<b>5/2005</b>		◆										
1517	Limited Deployment Decision Review	5/2005		◆										
1518	<b>Increment: Phase 1.1</b>	<b>8/2005</b>		◆										
1519	System Testing	8/2005		◆										
1520	<b>Increment: Phase 2 Full Deployment</b>	<b>10/2005</b>		◆										
1521	FDDR	10/2005		◆										
1522	<b>VISION</b>	<b>9/2008</b>			▬									
1523	<b>Key Milestones:</b>	<b>9/2008</b>			▬									
1524	Milestone A	9/2004	◆											
1525	Milestone C	9/2008					◆							
1526														
1527	<b>DFAS</b>	<b>9/2008</b>			▬									

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	
1528	<b>Key Systems</b>	<b>4/2007</b>													
1529	<b>FCP</b>	<b>4/2007</b>													
1530	<b>Key Milestones:</b>	<b>10/2006</b>													
1531	Complete AoA	1/2003													
1532	Milestone B	1/2004													
1533	Milestone C	2/2006													
1534	IOC	2/2006													
1535	FOC	10/2006													
1536	<b>Legacy Systems migrating to FCP</b>	<b>4/2007</b>													
1537	DJMS-AC	4/2007													
1538	DJMS-RC	4/2007													
1539	<b>Key Initiatives</b>	<b>9/2008</b>													
1540	<b>Disb HPO</b>	<b>9/2008</b>													
1541	<b>Key Milestones:</b>	<b>9/2008</b>													
1542	<b>Increment: Eliminate SRD-1</b>	<b>6/2006</b>													
1543	IOC	6/2006													
1544	<b>Increment: Eliminate CDS</b>	<b>9/2008</b>													
1545	FOC	9/2008													
1546	<b>Increment: Consolidate disbursing services and achieve standardization at fewer than the five current DFAS sites.</b>	<b>9/2008</b>													
1547	FOC	9/2008													
1548	<b>EC</b>	<b>9/2006</b>													
1549	<b>Key Milestones:</b>	<b>9/2006</b>													
1550	<b>Increment: Deploy WAWF to ARMY</b>	<b>9/2006</b>													
1551	FOC	9/2006													
1552															
1553	<b>DLA</b>	<b>8/2011</b>													
1554	<b>Key Systems</b>	<b>4/2011</b>													
1555	<b>BSM</b>	<b>9/2006</b>													
1556	<b>Key Milestones:</b>	<b>9/2006</b>													
1557	Milestone 0	12/1999													
1558	Complete AoA	2/2000													
1559	Milestone I/II	8/2000													
1560	<b>Increment: Release 1.0</b>	<b>8/2002</b>													
1561	Milestone C	8/2002													
1562	<b>Increment: Release 2.0</b>	<b>1/2005</b>													
1563	IOC	1/2005													
1564	<b>Increment: Release 2.2</b>	<b>9/2006</b>													
1565	Full-Rate Production Decision Review (FRPDR)	12/2005													
1566	FOC	9/2006													
1567	<b>Legacy Systems migrating to BSM</b>	<b>9/2006</b>													

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	
1568	DISMS	1/2005		◆											
1569	SAMMS	9/2006			◆										
1570	<b>BSM-Energy</b>	<b>6/2007</b>													
1571	<b>Key Milestones:</b>	<b>6/2007</b>													
1572	Milestone 0/I/II	11/1995													
1573	Base Level Operations - FOC	9/2001													
1574	Bulk Enterprise Level Operations - FOC	4/2003													
1575	FOC	6/2007				◆									
1576	<b>Increment: Base Level Operations</b>	<b>1/1997</b>													
1577	Milestone IIIa Base Level Operations	1/1997													
1578	<b>Increment: CONUS Bulk</b>	<b>5/2002</b>													
1579	Milestone IIIb Enterprise Level Operations - CONUS Bulk	5/2002													
1580	<b>Increment: CONUS PC&amp;S</b>	<b>5/2004</b>	◆												
1581	Full-Rate Production Decision Review (FRPDR)	5/2004	◆												
1582	<b>Increment: OCONUS (Bulk &amp; PC&amp;S)</b>	<b>5/2006</b>			◆										
1583	FRPDR for Enterprise Level OCONUS (Bulk & PC&S)	5/2006			◆										
1584	<b>Legacy Systems migrating to BSM-Energy</b>	<b>6/2007</b>				◆									
1585	DFAMS	6/2007				◆									
1586	<b>CFMS</b>	<b>4/2011</b>													
1587	<b>Key Milestones:</b>	<b>4/2011</b>													
1588	Milestone A	4/2003													
1589	Phase 'A' AOA	1/2004	▶												
1590	Milestone B	8/2004	◆												
1591	IOC	8/2006			◆										
1592	Phase 'B' AOA	9/2006			◆										
1593	Milestone C	3/2007				◆									
1594	FOC	4/2011												◆	
1595	<b>Legacy Systems migrating to CFMS</b>	<b>4/2011</b>													
1596	AFMIS	1/2009						◆							
1597	CFS	1/2009						◆							
1598	FSM afloat	4/2011												◆	
1599	MCFMIS	1/2009						◆							
1600	NFMIS	1/2009						◆							
1601	STORES NT	4/2005		◆											
1602	<b>DPMS</b>	<b>6/2006</b>													
1603	<b>Key Milestones:</b>	<b>6/2006</b>													
1604	<b>Increment: 1st Destination Optimization</b>	<b>5/2004</b>	▶												
1605	Milestone A	6/2002													
1606	Milestone B	10/2002													
1607	Integration Contract Award	8/2003													
1608	Complete AoA	3/2004	◆												

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1609	Milestone C	5/2004	◆											
1610	IOC	5/2004	◆											
1611	<b>Increment: 2nd Destination Optimization</b>	<b>5/2005</b>		◆										
1612	Additional Enhancements	5/2005		◆										
1613	Milestone C	5/2005		◆										
1614	<b>Increment: BSM Integration</b>	<b>8/2005</b>		◆										
1615	Additional Enhancements	8/2005		◆										
1616	Milestone C	8/2005		◆										
1617	<b>Increment: Reverse Logistics</b>	<b>6/2006</b>			◆									
1618	Milestone C	6/2006			◆									
1619	FOC	6/2006			◆									
1620	<b>RMP</b>	<b>6/2009</b>												
1621	<b>Key Milestones:</b>	<b>6/2009</b>												
1622	Milestone A	12/2003	◆											
1623	Fit-Gap Analysis Contract	9/2004	◆											
1624	Complete AoA	10/2005		◆										
1625	Milestone B	10/2005		◆										
1626	Integration Contract	3/2006			◆									
1627	Milestone C	2/2007				◆								
1628	IOC	6/2007				◆								
1629	FOC	6/2009						◆						
1630	<b>Legacy Systems migrating to RMP</b>	<b>6/2009</b>						◆						
1631	DAISY	6/2009						◆						
1632	BOSS Hazardous	6/2009						◆						
1633	<b>Key Initiatives</b>	<b>8/2011</b>												
1634	<b>CRM</b>	<b>8/2008</b>												
1635	<b>Key Milestones:</b>	<b>8/2008</b>												
1636	Milestone A	10/2002												
1637	Milestone B	9/2003												
1638	Complete AoA	12/2005			◆									
1639	Milestone C	2/2006			◆									
1640	IOC	3/2006			◆									
1641	FOC	8/2008						◆						
1642	<b>DLA IDE</b>	<b>8/2011</b>												
1643	<b>Key Milestones:</b>	<b>8/2011</b>												
1644	Milestone A	8/2001												
1645	Milestone B	6/2002												
1646	Complete AoA	1/2003												
1647	Milestone C	9/2005		◆										
1648	IOC	11/2005		◆										
1649	FOC	8/2011												◆

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1650	<b>P3I</b>	<b>3/2006</b>												
1651	<b>Key Milestones:</b>	<b>3/2006</b>			◆									
1652	P3I initiatives to be formalized	3/2006			◆									
1653	<b>PDMI</b>	<b>7/2011</b>												
1654	<b>Key Milestones:</b>	<b>7/2011</b>												
1655	Complete AoA	4/2003												
1656	Milestone A	8/2002												
1657	Milestone B	10/2003												
1658	Milestone C	5/2007				◆								
1659	IOC	5/2007				◆								
1660	FOC	7/2011								◆				
1661														
1662	<b>Navy</b>	<b>12/2011</b>												
1663	<b>Key Systems</b>	<b>12/2011</b>												
1664	<b>GCSS-MC</b>	<b>3/2008</b>												
1665	<b>Key Milestones:</b>	<b>3/2008</b>												
1666	<b>Increment: LCM Block 1 (Logistics Chain Management Block 1)</b>	<b>3/2008</b>												
1667	Milestone A	7/2004	◆											
1668	Milestone B	11/2005		◆										
1669	IOC	11/2007				◆								
1670	Milestone C	5/2007				◆								
1671	FOC	3/2008					◆							
1672	<b>Legacy Systems migrating to GCSS-MC</b>	<b>3/2008</b>					◆							
1673	ATLASS I	3/2008					◆							
1674	MIMMS	3/2008					◆							
1675	PC MIMM	3/2008					◆							
1676	SASSY	3/2008					◆							
1677	<b>Navy Cash</b>	<b>10/2008</b>												
1678	<b>Key Milestones:</b>	<b>10/2008</b>												
1679	Milestone A	6/1999												
1680	Milestone B	11/2000												
1681	Complete AoA	12/2002												
1682	Milestone C	6/2003												
1683	IOC	1/2004	▶											
1684	FOC	10/2008					◆							
1685	<b>Legacy Systems migrating to Navy Cash</b>	<b>10/2008</b>					◆							
1686	ATMs-At-Sea	10/2008					◆							
1687	<b>NAVY ERP</b>	<b>12/2011</b>												
1688	<b>Key Milestones:</b>	<b>12/2011</b>												
1689	<b>Increment: Financial &amp; Regional Maintenance Release</b>	<b>12/2011</b>												
1690	Milestone A	8/2004	◆											

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1691	Milestone B	8/2004	◆											
1692	Retire SMART Pilot	9/2005		◆										
1693	Begin Regional Maintenance Center Deployments	9/2006			◆									
1694	Begin Echelon I Deployment	9/2006			◆									
1695	Milestone C	9/2006			◆									
1696	Retire NEMAIS Pilot	9/2006			◆									
1697	IOC	10/2006			◆									
1698	Retire CABRILLO Pilot	9/2007				◆								
1699	Retire SIGMA Pilot	9/2007				◆								
1700	Begin Echelon II Headquarters Deployments	10/2007				◆								
1701	Begin Warfare Center Deployments	10/2007				◆								
1702	FOC	12/2011									◆			
1703	<b>Increment: Regional Supply Release</b>	<b>9/2008</b>					◆							
1704	Begin Fleet Regional Supply Centers	8/2008					◆							
1705	IOC	8/2008					◆							
1706	FOC	9/2008					◆							
1707	<b>Increment: Wholesale Supply Release</b>	<b>9/2007</b>				◆								
1708	Begin Inventory Control Point Deployments	7/2007				◆								
1709	IOC	7/2007				◆								
1710	FOC	9/2007				◆								
1711	<b>Legacy Systems migrating to NAVY ERP</b>	<b>9/2011</b>												
1712	5 YEAR DEMAND CALCULATOR	9/2011												◆
1713	A&P REPORTS	9/2009						◆						
1714	A2E-A4E SUPPLY DIRECTIVE	9/2011												◆
1715	A3910	9/2006			◆									
1716	ABM	9/2011												◆
1717	ABS	9/2011												◆
1718	ACCESS	9/2011												◆
1719	ACCOM STORAGE	9/2011												◆
1720	ACIP	9/2009												
1721	ADEPT SERIES	9/2008					◆							
1722	ADS-AIR	9/2007				◆								
1723	AIM	9/2008					◆							
1724	AIMS	9/2008					◆							
1725	AIMTC	9/2011												◆
1726	AIR FLASK TRACKING DB	9/2009						◆						
1727	ALMARS	9/2011												
1728	ALTMIS	9/2009						◆						
1729	ALTP	9/2011												◆
1730	AMP	9/2009												
1731	ANCHORS NC	9/2009						◆						

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1732	APN IFL MIS	9/2009						◆						
1733	APN-6 BUD REQ	9/2009						◆						
1734	APN-6 IFL	9/2009						◆						
1735	APNE	9/2009						◆						
1736	ARO	9/2011								◆				
1737	AS/RS	9/2011								◆				
1738	ASI	9/2011								◆				
1739	ASIPS	9/2008					◆							
1740	ASM	9/2011								◆				
1741	ASP	9/2011								◆				
1742	ATAC-NVY	9/2009						◆						
1743	ATS	9/2011								◆				
1744	AUTODOC	9/2009						◆						
1745	B15RVW	9/2011								◆				
1746	BAP	9/2011								◆				
1747	BARTENDER BARCOED LABELING	9/2009						◆						
1748	BDI	9/2008												
1749	BEANS	9/2009						◆						
1750	BPS	9/2009						◆						
1751	BPS	9/2011								◆				
1752	BRF	9/2011								◆				
1753	BRIO QUERY	9/2011												
1754	BSA	9/2009						◆						
1755	BTS - WD	9/2008					◆							
1756	Budget - NEDU	9/2011								◆				
1757	BUYOUT	9/2011												
1758	C10 80 COLUMN MAINTENANCE	9/2011								◆				
1759	C10 ERROR/INPUTS	9/2011												
1760	C14 80 COLUMN MAINTENANCE	9/2011												
1761	C14LBC	9/2011								◆				
1762	CABRILLO	9/2008					◆							
1763	CASTS	9/2008					◆							
1764	CBTIMS	9/2011								◆				
1765	CCRP FEEDBACK/INIT	9/2009						◆						
1766	CCRP MANAGEMENT DB	9/2009						◆						
1767	CDASS	9/2008					◆							
1768	CDB WEB	9/2009						◆						
1769	CDMS/DMS	9/2008					◆							
1770	CDT	9/2009						◆						
1771	CED	9/2011								◆				
1772	CERAP	9/2011								◆				

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1773	CLIFAFS	9/2011								◆				
1774	CMAS	9/2009						◆						
1775	CMBUS	9/2011								◆				
1776	CMIS	9/2011								◆				
1777	CMSTAT	9/2009						◆						
1778	COBRA	9/2009						◆						
1779	COMPAS	9/2007				◆								
1780	CORPORATE DATA BASE	9/2011								◆				
1781	CPRS	9/2011								◆				
1782	CRMM HISTORY	9/2009						◆						
1783	CSAT	9/2011								◆				
1784	CSM	9/2009						◆						
1785	CSSR CYCLIC TRIGGERS	9/2011								◆				
1786	CTS - SSC CH	9/2009						◆						
1787	CWPS - SEA	9/2011								◆				
1788	DCOSIMS	9/2009						◆						
1789	DEMIL	9/2011								◆				
1790	DISPOSAL	9/2011								◆				
1791	DISPOSAL TRACKING SYSTEM	9/2011								◆				
1792	DMTS AWP INTEGRATION SUPPORT	9/2009						◆						
1793	DOCUMENT CONTROL	9/2011								◆				
1794	DPMETRICS	9/2011								◆				
1795	DRATS	9/2011								◆				
1796	DRRT	9/2011								◆				
1797	DSSQR	9/2011								◆				
1798	EBIS-SEA	9/2011								◆				
1799	ERCM	9/2009						◆						
1800	ERL PROGRAM	9/2009						◆						
1801	ERMS	9/2011								◆				
1802	FCT	9/2008					◆							
1803	FHT	9/2011								◆				
1804	FIRST	9/2011								◆				
1805	FIS	9/2007				◆								
1806	FITS	9/2008					◆							
1807	FMD	9/2009						◆						
1808	FMIS - NSLC	9/2010							◆					
1809	FMIS 2000/UPGRADE	9/2006			◆									
1810	FMT	9/2011								◆				
1811	FMT - TRAINING	9/2011								◆				
1812	FMT.MCH	9/2011								◆				
1813	FTP NNPI	9/2009						◆						

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1814	FWTS	9/2011								◆				
1815	G02APU	9/2011								◆				
1816	G02PR12	9/2011								◆				
1817	GENUS TRAINING	9/2009						◆						
1818	GIBBS	9/2008					◆							
1819	HEADQUARTERS FORMS	9/2008					◆							
1820	HEDRS	9/2011								◆				
1821	IA	9/2008					◆							
1822	IBC	9/2009						◆						
1823	ICB	9/2011								◆				
1824	ICF	9/2011								◆				
1825	ICP	9/2011								◆				
1826	IHD Locals	9/2011								◆				
1827	IMPS	9/2011								◆				
1828	IMTK	9/2011								◆				
1829	INCMAS	9/2011								◆				
1830	INFORM	9/2008					◆							
1831	IP - NSWC - CD	9/2011								◆				
1832	IPMS - Corona	9/2011								◆				
1833	IPMS WEB	9/2007				◆								
1834	iRAPS	9/2011								◆				
1835	ISD	9/2011								◆				
1836	J15PPI	9/2011								◆				
1837	J50 BBS	9/2011								◆				
1838	JONAS	9/2011								◆				
1839	LAR DATABASE FOR 688 CLASS	9/2009						◆						
1840	LCU	9/2011								◆				
1841	LMS21	9/2011								◆				
1842	LOFTWARE	9/2011								◆				
1843	LRC MAINTENANCE	9/2011								◆				
1844	LRS	9/2010							◆					
1845	M1134A4	9/2011								◆				
1846	MALF	9/2011								◆				
1847	MANA	9/2007				◆								
1848	MAPL	9/2011								◆				
1849	MEASURE NAME AND ADDRESS QUERY	9/2008					◆							
1850	MFCS - Retail Afloat	9/2011								◆				
1851	MFCS PX02/04	9/2011								◆				
1852	MFCS-PX06	9/2011								◆				
1853	MICRO PMR	9/2009						◆						
1854	MOMENTUM	9/2010							◆					

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1855	MPCR	9/2009						◆						
1856	MPDCR	9/2009						◆						
1857	MPSTAT	9/2009						◆						
1858	MRIL	9/2011								◆				
1859	MRMS	9/2009						◆						
1860	MTPSI	9/2011								◆				
1861	NAVSUP HQCPB	9/2009						◆						
1862	NCB	9/2007				◆								
1863	NEMAIS	9/2006			◆									
1864	NOMBERS	9/2008					◆							
1865	NSWCDD LOCATOR	9/2009						◆						
1866	OMEPS	9/2011								◆				
1867	ON-CENTER MATERIALS DELEVERY TRACKING SYSTEM	9/2011								◆				
1868	ONLINE COMPUTER INFORMATION EXCHANGE	9/2011								◆				
1869	ONLINE CSSR	9/2011								◆				
1870	OSP	9/2011								◆				
1871	OTFw	9/2011								◆				
1872	OTS	9/2009						◆						
1873	P3	9/2009						◆						
1874	P3E 3.5	9/2008					◆							
1875	PACE-PIO	9/2011								◆				
1876	PARM	9/2011								◆				
1877	PARS	9/2011								◆				
1878	PARTS	9/2009						◆						
1879	PATS	9/2011								◆				
1880	PB VIEWS	9/2009						◆						
1881	PBAS-FD	9/2007				◆								
1882	PC	9/2011								◆				
1883	PC TRAVEL	9/2011								◆				
1884	PCRIMS	9/2011								◆				
1885	PCS	9/2009						◆						
1886	PCS CODE 807	9/2011								◆				
1887	PCS CODE 809	9/2011								◆				
1888	PDCNLOG	9/2011								◆				
1889	PDM	9/2011								◆				
1890	PDREP - WEB ENABLED	9/2009						◆						
1891	PERSONNEL MOBILITY	9/2011								◆				
1892	PHIMS	9/2009						◆						
1893	PLS	9/2007				◆								
1894	PMIS	9/2011								◆				
1895	PMP NEW	9/2009						◆						

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1896	PMS MATE	9/2007				◆								
1897	PMS TASK TRACKING	9/2009						◆						
1898	PMT NEMAIS WEB SITE	9/2008					◆							
1899	POM	9/2009						◆						
1900	PPR MANAGEMENT	9/2011								◆				
1901	PPR/TIR MAINTEN	9/2011								◆				
1902	PREDICTED STOCK OUT	9/2011								◆				
1903	PRIMAVERA	9/2009						◆						
1904	PRISMS	9/2009						◆						
1905	PROVSCRN	9/2011								◆				
1906	PS	9/2011								◆				
1907	PSICP	9/2011								◆				
1908	PSSR FOR PMS (VIRGINIA)	9/2009						◆						
1909	PWPROPER	9/2011								◆				
1910	QAIL	9/2009						◆						
1911	QH2	9/2011								◆				
1912	RAPID	9/2007				◆								
1913	REPAIR SNAPSHOT	9/2011								◆				
1914	REQUISITION HISTORY	9/2011								◆				
1915	RHICS	9/2009						◆						
1916	RIMS(PH) - F	9/2005		◆										
1917	RIPS	9/2011								◆				
1918	RMAIS-C/S	9/2009						◆						
1919	RMF	9/2011								◆				
1920	RMME	9/2011								◆				
1921	ROR	9/2011								◆				
1922	ROR	9/2008					◆							
1923	RPD (DON SEA)	9/2011								◆				
1924	RTAT	9/2011								◆				
1925	RTS - SSC Norfolk	9/2009						◆						
1926	SAP FIMS+	9/2008					◆							
1927	SAP FIMS+	9/2006			◆									
1928	SCC - Carderock	9/2011								◆				
1929	SCS	9/2011								◆				
1930	SDF	9/2011								◆				
1931	SDF AUDIT	9/2011								◆				
1932	SHIPS NEW CONSTRUCTION DATABASE	9/2011								◆				
1933	SIDEWINDER (AIM-9) TARGETING DATABASE	9/2011								◆				
1934	SIDEWINDER MK 13 MOD 2 DATABASE	9/2011								◆				
1935	SIGMA	9/2007				◆								
1936	SKEDA	9/2009						◆						

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1937	SMART	9/2005		◀										
1938	SMD	9/2011								◆				
1939	SMS	9/2009						◆						
1940	SNCTP-DB	9/2009						◆						
1941	SOS	9/2010							◆					
1942	SP ENGINEERING INTRANET	9/2011								◆				
1943	SPFS	9/2009						◆						
1944	SPIPL	9/2007				◆								
1945	SPM	9/2011								◆				
1946	SSR	9/2011								◆				
1947	STARS-HCM	9/2011								◆				
1948	STP	9/2011								◆				
1949	STRAT	9/2011								◆				
1950	STRIPES	9/2009						◆						
1951	SUBMEPP BUD PREP	9/2009						◆						
1952	SUBMEPP FMS	9/2009						◆						
1953	SUBMEPP-M&SWP	9/2009						◆						
1954	SUBMEPP-SHIPALT HISTORY ARCHIVE DB	9/2009						◆						
1955	SUPDIR	9/2011								◆				
1956	SUPMIS	9/2007				◆								
1957	SURVRT	9/2011								◆				
1958	SWIMS	9/2011								◆				
1959	SYSTAT	9/2011								◆				
1960	TC3	9/2011								◆				
1961	TEST EQUIPMENT ARCHIVE SET	9/2011								◆				
1962	THF	9/2011								◆				
1963	THF	9/2011								◆				
1964	THF DMD CUST - WEB	9/2011								◆				
1965	TIR	9/2011								◆				
1966	TME DATABASE SUITE	9/2011								◆				
1967	TMX WEB-BASED DATABASE	9/2011								◆				
1968	TOMCAT	9/2009						◆						
1969	TOPS	9/2009						◆						
1970	TRACKWISE	9/2011								◆				
1971	TRANSREG	9/2007				◆								
1972	TRD	9/2009						◆						
1973	TRI-ME	9/2007				◆								
1974	TRIPER PROGRAM CHANGEOUTS PROGRAM	9/2009						◆						
1975	TRIREFFAC BANGOR RFT RPTG	9/2009						◆						
1976	UADPS-ICP	9/2009						◆						
1977	UADPS-SP	9/2011								◆				

Enterprise Transition Plan, Appendix J: System Transition Schedule

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
1978	UOT - RAOR	9/2008					◆							
1979	UOT PCOR	9/2008					◆							
1980	V-STARS	9/2009						◆						
1981	WIPP	9/2011								◆				
1982	WIS	9/2011								◆				
1983	WLM/DR	9/2009						◆						
1984	WMS	9/2011								◆				
1985	WO SURV DATA - MMC RESULTS	9/2011								◆				
1986	WORK TO TEST MATRIX DB	9/2009						◆						
1987	WSMETRIC	9/2011								◆				
1988	WSSP	9/2011								◆				
1989	YOUNG VALVE HISTORY	9/2009						◆						
1990	<b>NTCSS</b>	<b>9/2000</b>												
1991	<b>Key Milestones:</b>	<b>9/2000</b>												
1992	MS I NTCSS Optimization	10/1995												
1993	MS 0 NTCSS SDM	4/1995												
1994	MS II NTCSS Optimized BPR Approved	4/1997												
1995	MS IIIB Optimized R-ADM	3/2000												
1996	MS IIIC Optimized IMA	3/2000												
1997	MS IIIA Optimized OMMS-NG and R-Supply	9/2000												
1998	<b>TFAS</b>	<b>10/2010</b>												
1999	<b>Key Milestones:</b>	<b>9/2002</b>												
2000	Milestone A	3/2000												
2001	Milestone C	7/2002												
2002	IOC	9/2002												
2003	<b>Legacy systems migrating to TFAS</b>	<b>10/2010</b>												
2004	AWARDS	12/2008						◆						
2005	DPRIS-MC	6/2006												
2006	DTMS & MCASSP	12/2005												
2007	Impromptu	12/2005												
2008	P&A Module	12/2008								◆				
2009	PES/APES	5/2005						◆						
2010	RAPTRS	7/2010												
2011	RDA	10/2008								◆				
2012	RDOL	10/2010												
2013	ROWS	12/2009												
2014	S&R	12/2009												
2015	TFRS	4/2007												
2016	TRNG	12/2007												
2017	<b>Key Initiatives</b>	<b>9/2008</b>												
2018	<b>AIT</b>	<b>9/2006</b>												

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
2019	<b>Key Milestones:</b>	<b>9/2006</b>												
2020	Develop SECNAV Policy	11/2005												
2021	Determine passive RFID application	12/2005												
2022	Develop POM 08 Submission	12/2005												
2023	Continue COCOM Support for aRFID	9/2006												
2024	<b>EA-21</b>	<b>1/2007</b>												
2025	<b>Key Milestones:</b>	<b>1/2007</b>												
2026	Increase CPARS usage at DON Commands to achieve the goal of 100% compliance with FAR Parts 15 and 42	9/2006												
2027	Convert CPARS platform from Silver Stream (which is no longer supported) to the Apache/Tomcat platform	9/2006												
2028	Transfer PRBuilder Ownership to Marine Corps	12/2006												
2029	Develop plan to transition PRB-UI to the Marine Corps	12/2006												
2030	Support PPIRS SR Module pilot test and prepare for DoD and Federal-wide roll out as an IAE initiative	12/2006												
2031	Execute application-programming enhancements as agreed to by the UI IPT	1/2007												
2032	<b>MC FII</b>	<b>9/2008</b>												
2033	<b>Key Milestones:</b>	<b>9/2008</b>												
2034	<b>Increment: Discovery &amp; Correction</b>	<b>9/2006</b>												
2035	Final Policy Implemented	9/2006												
2036	Complete Analysis Identify and Implement business process solutions	9/2006												
2037	Implement MFEAT Team	9/2006												
2038	<b>Increment: Baseline Valuations</b>	<b>9/2006</b>												
2039	Complete Inventory valuations	9/2006												
2040	<b>Increment: Pre-Audit Assessments</b>	<b>9/2007</b>												
2041	Complete Validations, Assessments & Audits	9/2007												
2042	<b>Increment: Validations</b>	<b>9/2007</b>												
2043	Complete Validations, Assessments & Audits	9/2007												
2044	<b>Increment: Audits</b>	<b>9/2008</b>												
2045	Complete Validations, Assessments & Audits	9/2008												
2046	<b>NMCI</b>	<b>6/2006</b>												
2047	<b>Key Milestones:</b>	<b>6/2006</b>												
2048	IOC	5/2002												
2049	Decision Point 1 (DP 1) Complete Initial OT&E	5/2002												
2050	DP II A/B Complete Operational Assessment	2/2003												
2051	DP III Complete OpEval/ASD NII Remands oversight of NMCI to DON	9/2004												
2052	FOC	6/2006												
2053														
2054	<b>USTRANSCOM</b>	<b>9/2010</b>												
2055	<b>DEAMS</b>	<b>9/2010</b>												

ID	Task Name	Finish	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015
2056	<b>Key Milestones:</b>	<b>3/2009</b>												
2057	<b>Increment: Increment 1 USTRANSCOM</b>	<b>2/2008</b>												
2058	Complete AoA	1/2005		◆										
2059	Milestone A	4/2005		◆										
2060	Milestone B	1/2007				◆								
2061	Milestone C	9/2007					◆							
2062	IOC	9/2007					◆							
2063	FOC	2/2008					◆							
2064	<b>Increment: Increment 2 USAF</b>	<b>3/2009</b>												
2065	Milestone A	1/2007				◆								
2066	Milestone B	2/2008					◆							
2067	Milestone C	3/2009						◆						
2068	IOC	3/2009						◆						
2069	<b>Legacy Systems migrating to DEAMS</b>	<b>9/2010</b>												
2070	ABSS	3/2009						◆						
2071	ASIFICS	10/2006				◆								
2072	BARS	9/2010							◆					
2073	CPAS	12/2004	◆											
2074	FMS	9/2007				◆								
2075	GAFS	9/2010							◆					
2076	GAFS-R	9/2010							◆					
2077	IAPS	9/2010							◆					
2078	TFMS-M	9/2007				◆								
